


**पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - II ( भूमि अधिग्रहण प्रगति माह अप्रैल, 2014 )**

**WDFC – PHASE – II (Land Acquisition Progress for the Month of April 2014)**

	( Kms)	22	53	60	37	72	138	45
	Area (Ha.)	134	330	248	65	91	368	74
20A (Ha.)		134	330	248	65	91	368	74
20E (Ha.)		134	330	248	65	91	368	74
20F (Ha.)		134	327	238	50	69	364	74
Award Declared (Cr.)		35	117	452	33	26	480	5
Disbursed (Cr.)		34	99	330	26	19	150	3
Land Taken over (Ha.)		133	276	174	39	50	114	0
Arbitration Cases No.		-	-	154	-	-	-	-

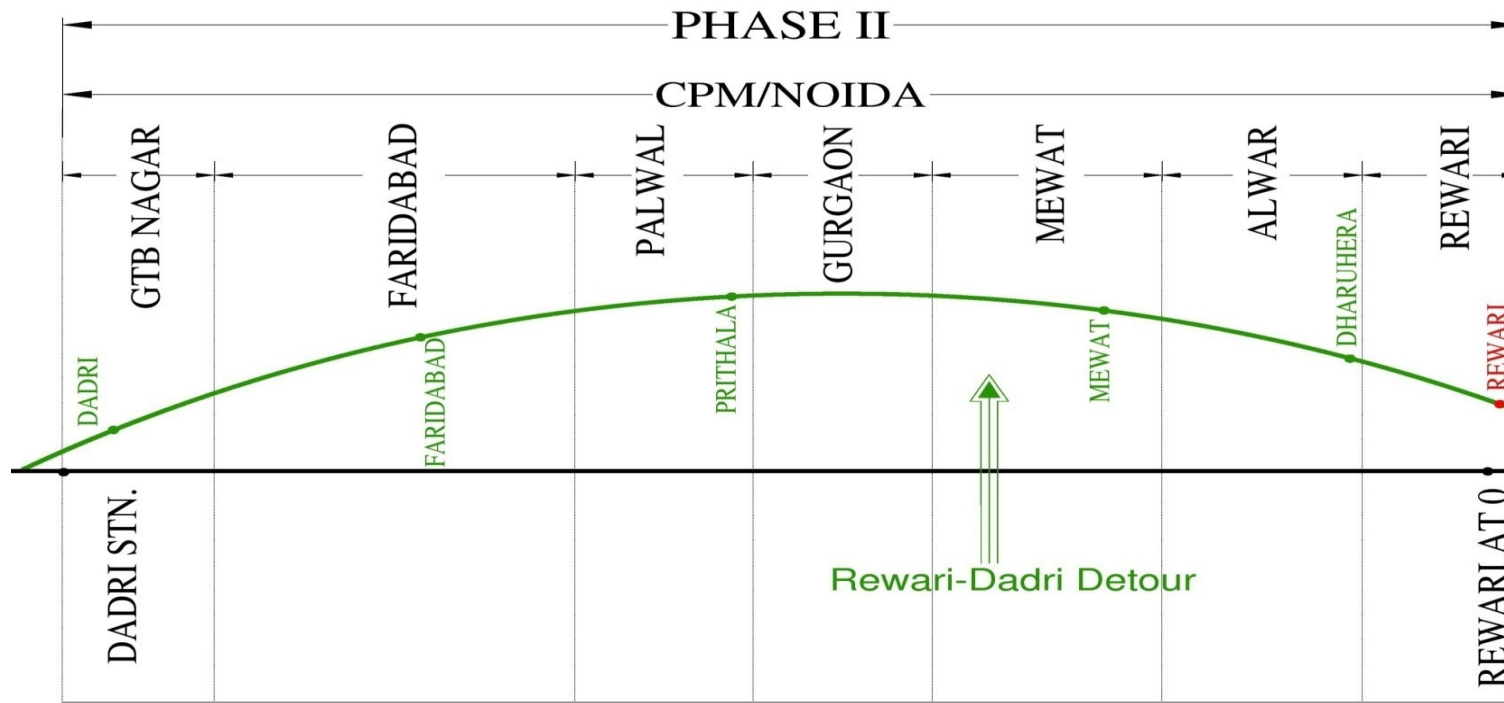

पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - II ( भूमि अधिग्रहण प्रगति माह अप्रैल, 2014 )

WDFC – PHASE – II (Land Acquisition Progress for the Month of April 2014)

	( Kms)	14	44	14	12	21	16	20
Area (Ha.)	102	255	129	75	159	95	127	
20A (Ha.)	102	255	129	75	159	95	127	
20E (Ha.)	102	178	128	75	158	95	127	
20F (Ha.)	99	176	125	73	154	90	124	
Award Declared (Cr.)	217	369	270	137	134	114	123	
Disbursed (Cr.)	156	318	231	106	123	60	114	
Land Taken over (Ha.)	72	-	-	-	-	-	114	
