


		पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - I (भूमि अधिग्रहण प्रगति)						
		WDFC - PHASE – I (Land Acquisition Progress)						
Scope	(Kms)	34	46	2	85	5	100	98
	Area (Ha.)	154	98	7	330	6	442	349
20A (Ha.)		154	98	7	330	6	442	349
20E (Ha.)		154	98	7	330	6	442	349
20F (Ha.)		154	98	7	327	6	421	349
Award Declared (Cr.)		151	82	3	33	0	27	79
Disbursed (Cr.)		145	82	2	31	0	26	74
Land Taken over (Ha.)		149	98	6	309	6	406	327

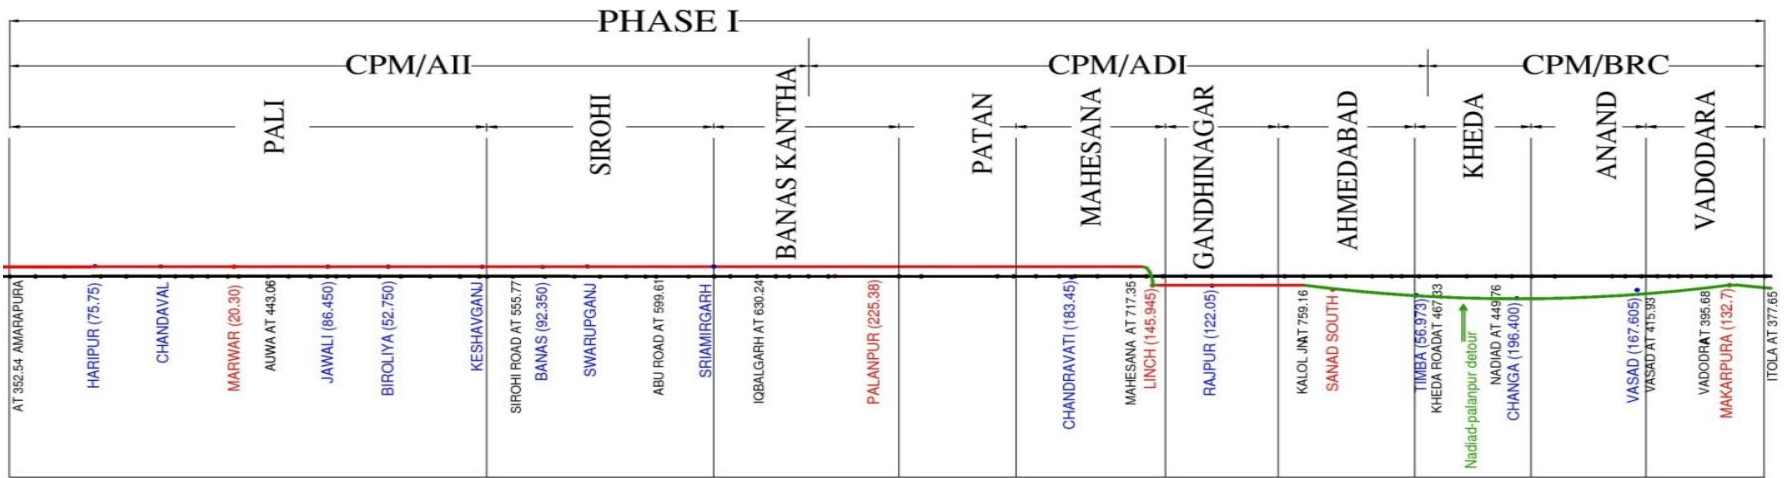

पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - I (भूमि अधिग्रहण प्रगति)

WDFC – PHASE – I (Land Acquisition Progress)

	(Kms)	196	65	77	12	64	30	35	29	43	32
	Area (Ha.)	546	142	353	16	166	189	312	166	290	270
20A (Ha.)		546	142	406	16	166	189	312	166	290	270
20E (Ha.)		546	142	30	16	166	189	312	166	290	270
20F (Ha.)		546	142	93	16	165	188	312	166	290	270
Award Declared (Crts.)		20	35	39	4	99	87	121	12	108	169
Disbursed (Crts.)		20	34	66	3	86	81	81	9	95	164
Land Taken over (Ha.)		524	140	258			177	209	133	255	261
