


Scope	पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - I (भूमि अधिग्रहण प्रगति)							
	WDFC - PHASE – I (Land Acquisition Progress)							
	(Kms)	34	46	2	79	5	98	98
Area (Ha.)	155	98	7	316	6	416	342	
20A (Ha.)	155	98	7	316	6	416	342	
20E (Ha.)	155	98	7	316	6	416	342	
20F (Ha.)	155	98	7	316	6	416	342	
Award Declared (Cr.)	153	82	3	37	0	31	92	
Disbursed (Cr.)	141	82	2	35	0	30	76	
Land Taken over (Ha.)	143	98	6	297	6	402	283	

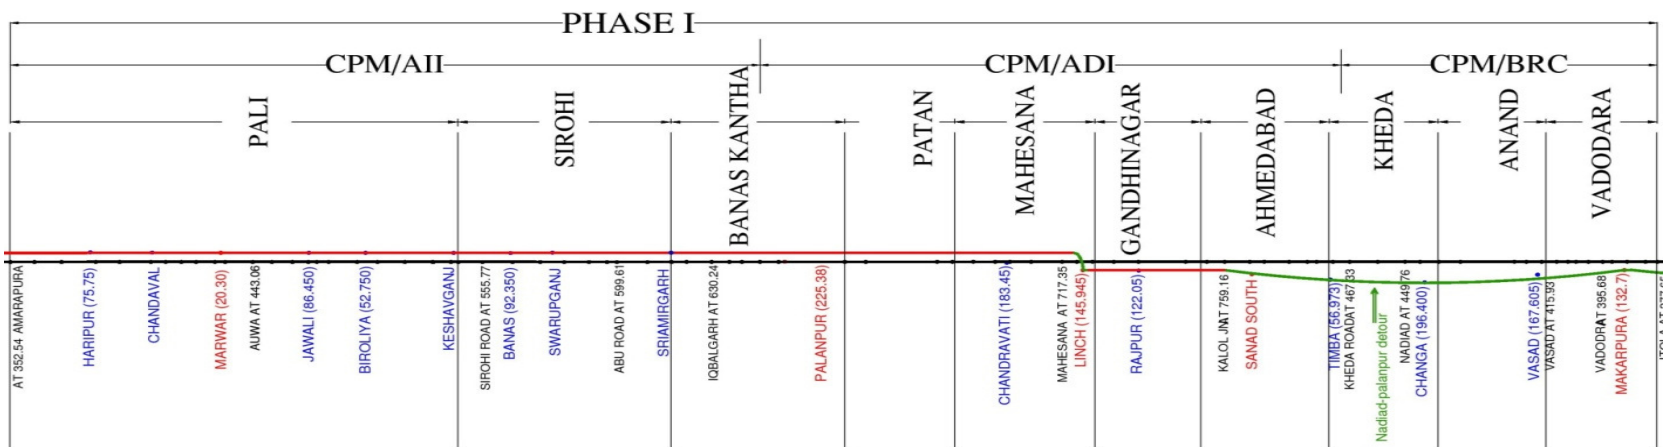

पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - I (भूमि अधिग्रहण प्रगति)

WDFC – PHASE – I (Land Acquisition Progress)

	(Kms)	195	65	77	12	64	30	35	29	43	32
	Area (Ha.)	546	140	284	15	166	189	308	166	288	280
20A (Ha.)		546	140	284	15	149	168	287	148	267	245
20E (Ha.)		546	140	236	15	145	168	287	148	267	245
20F (Ha.)		546	140	216	15	146	99	286	147	267	245
Award Declared (Cr.)		29	39	137	3	89	39	115	11	97	297
Disbursed (Cr.)		27	38	86	3	71	18	70	8	71	289
Land Taken over (Ha.)		512	137	136			46	175	106	196	239
