


Scope	पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - I ( भूमि अधिग्रहण प्रगति माह अप्रैल, 2014 )							
	WDFC -Phase-I (Land Acquisition Progress for the Month of April 2014)							
	(Kms)	34	46	2	79	5	98	98
Area (Ha.)	141	93	6	328	6	461	366	
20A (Ha.)	141	93	6	328	6	461	366	
20E (Ha.)	141	93	6	328	6	461	366	
20F (Ha.)	141	93	6	328	6	461	366	
Award Declared (Cr.)	152	82	3	37	0	31	91	
Disbursed (Cr.)	137	81	2	34	0	30	71	
Land Taken over (Ha.)	128	92	5	306	6	444	288	
Arbitration Cases No.	-	-	-	-	-	-	-	

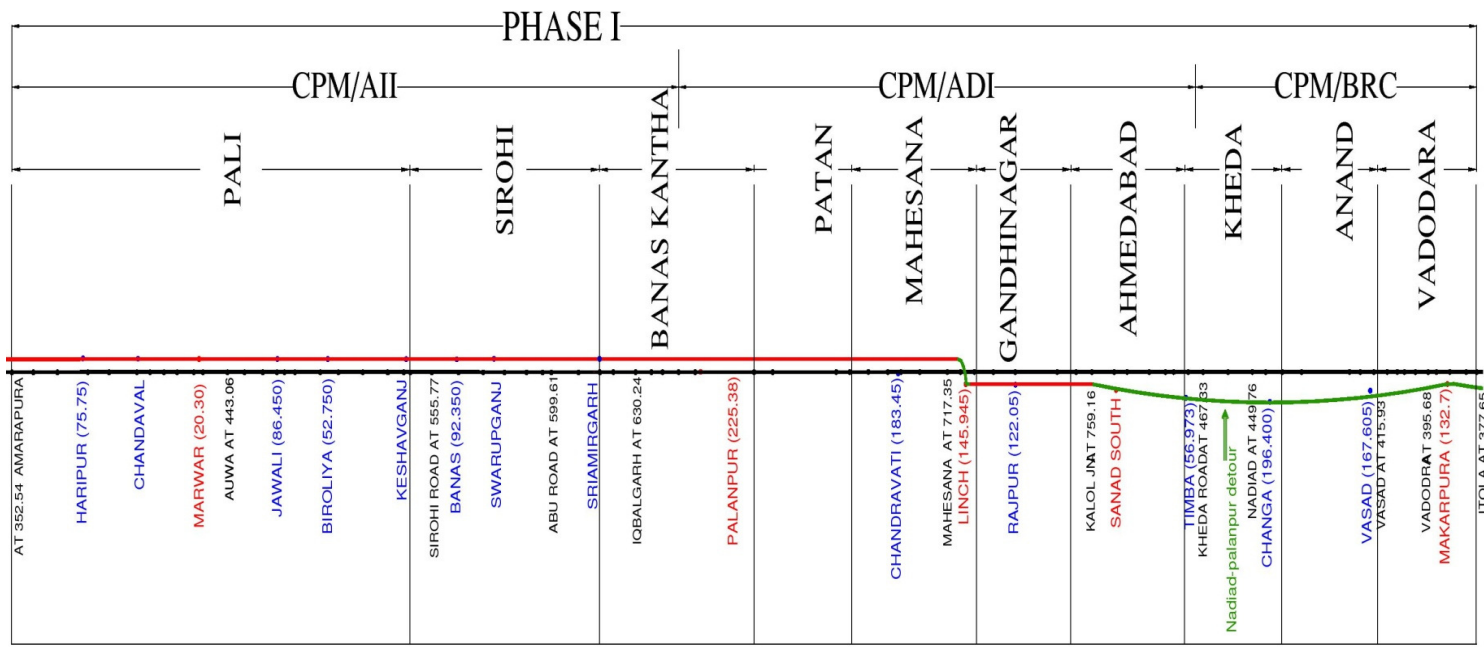

**पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - I ( भूमि अधिग्रहण प्रगति माह अप्रैल, 2014 )**

**WDFC – PHASE – I (Land Acquisition Progress for the Month of April 2014)**

	( Kms)	196	65	64	11	64	30	35	27	44	32
	Area (Ha.)	524	137	150	22	189	181	280	164	275	284
20A (Ha.)		524	137	150	22	189	181	280	164	275	284
20E (Ha.)		524	137	150	22	165	181	268	164	275	284
20F (Ha.)		524	137	150	19	165	117	268	163	274	284
Award Declared (Cr.)		33	39	27	4	81	31	115	10	98	307
Disbursed (Cr.)		33	35	22	3	8	13	47	6	69	302
Land Taken over (Ha.)		516	124	122			49	109	95	194	280
Arbitration Cases			-	1	-	-	-	-	-	-	-
