


WDFC – PHASE – II (Land Acquisition Progress May, 2021)

	(Kms)	22	52	60	37	72	34	39
Area (Ha.)		133	328	209	65	77	68	78
20A (Ha.)		133	328	209	65	77	68	78
20E (Ha.)		133	328	209	65	77	68	78
20F (Ha.)		133	328	209	63	75	67	77
Award Declared (Cr.)		42.56	191.21	653.26	56.79	82.88	595.04	84.03
Disbursed (Cr.)		42.22	177.44	633.23	50.06	69.73	415.81	42.07
Land Taken over PAP (Ha.)		146.51	322.16	184.77	36.94	57.58	50.34	8.62

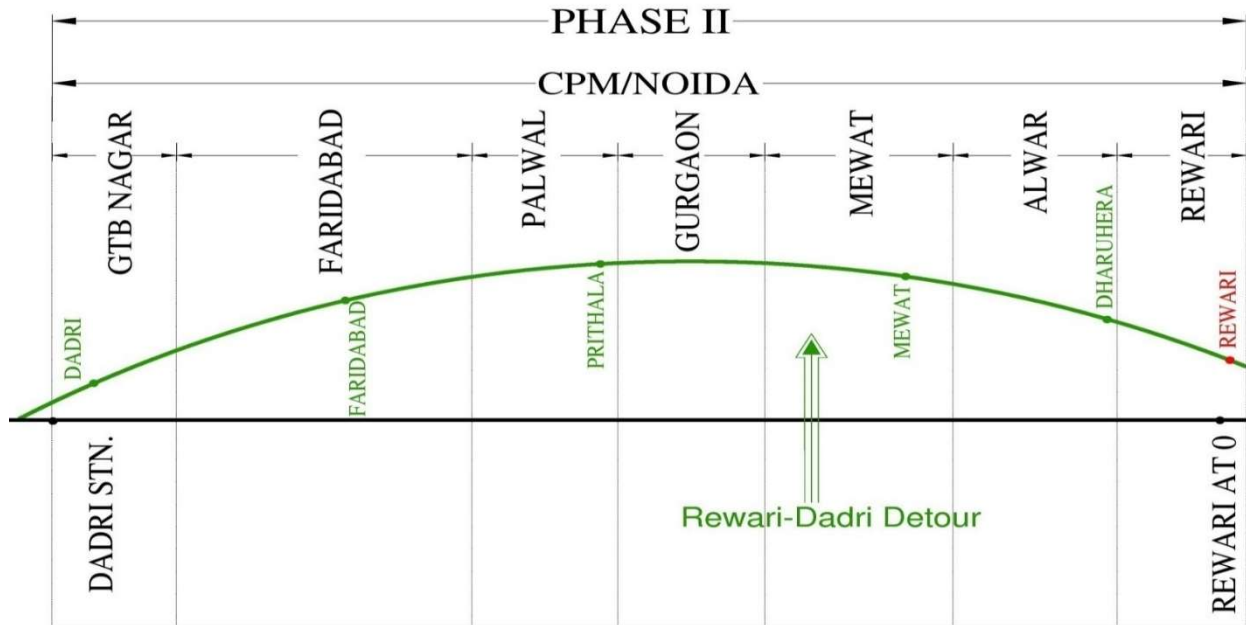

WDFC – PHASE – II (Land Acquisition Progress May, 2021)								
	(Kms)	19	28	15	12	20	16	20
	Area (Ha.)	175	207	127	77	163	132	145
20A (Ha.)	175	207	127	77	163	132	145	
20E (Ha.)	175	207	127	77	163	132	145	
20F (Ha.)	175	207	127	77	163	132	145	
Award Declared (Cr.)	710.77	553.26	365.53	201.59	284.63	267.17	198.35	
Disbursed (Cr.)	694.59	534.44	341.78	201.29	260.08	261.69	196.38	
Land Taken over PAP (Ha.)	89.08	200.09	127.00	76.14	154.76	76.23	142.40	
