


WDFC - PHASE – I (Land Acquisition Progress May, 2021)								
Scope	(Kms)	34	46	2	85	5	101	98
	Area (Ha.)	154	98	7	330	6	443	349
20A (Ha.)	154	98	7	330	6	443	349	
20E (Ha.)	154	98	7	330	6	443	349	
20F (Ha.)	154	98	7	330	6	443	349	
Award Declared (Cr.)	164.23	100.29	3.52	60.20	0.50	46.25	142.57	
Disbursed (Cr.)	161.54	95.68	2.82	56.58	0.49	45.92	130.03	
Land Taken over PAP (Ha.)	151.70	98.62	7.20	301.28	5.84	353.64	274.80	

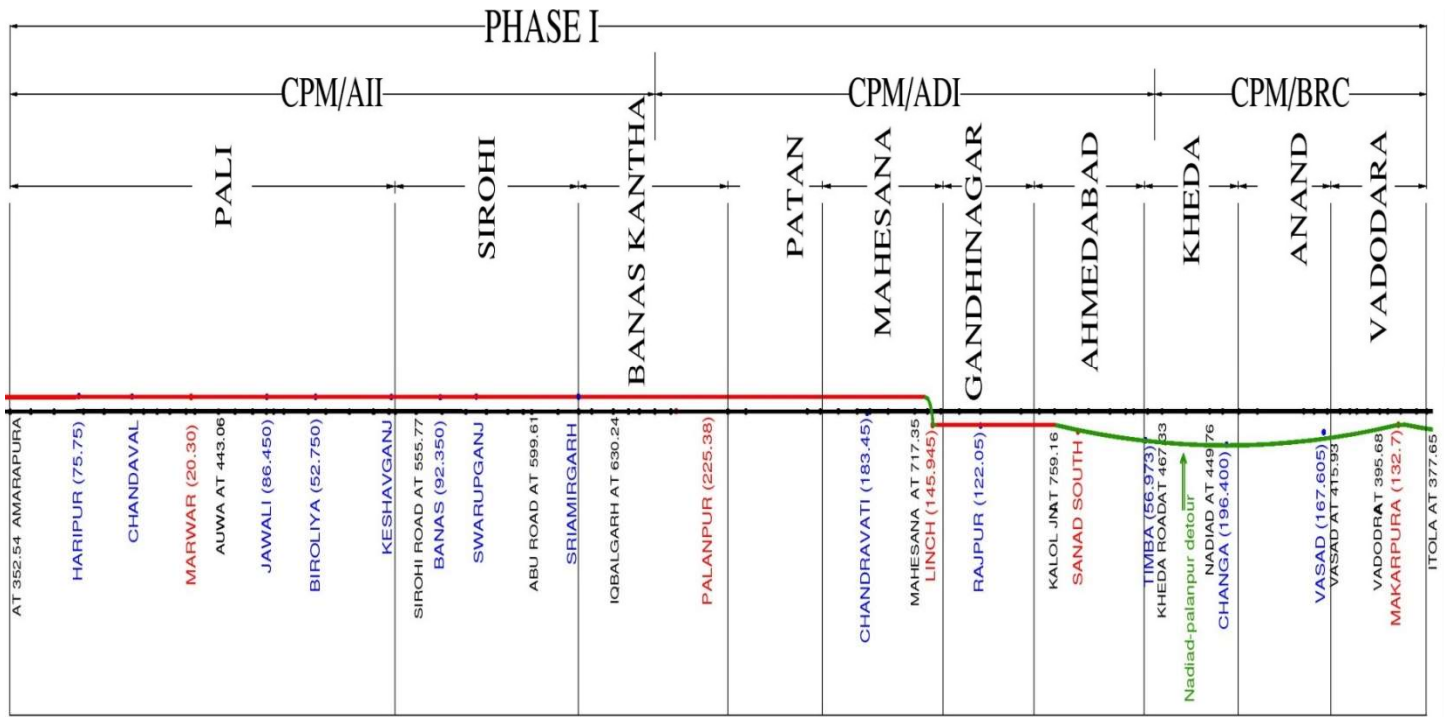

WDFC – PHASE – I (Land Acquisition Progress May, 2021)

	(Kms)	196	65	77	12	64	30	35	29	43	32
	Area (Ha.)	546	142	231	16	166	189	312	166	291	270
20A (Ha.)		546	142	231	16	166	189	312	166	291	270
20E (Ha.)		546	142	231	16	166	189	312	166	291	270
20F (Ha.)		546	142	231	16	166	189	312	166	290	270
Award Declared (Cr.)		35.84	62.70	113.88	5.46	117.51	127.60	131.30	22.52	128.15	296.97
Disbursed (Cr.)		34.30	60.98	111.36	5.43	110.49	122.18	127.95	18.35	116.0	293.86
Land Taken over PAP (Ha.)		317.93	87.47	198.88	14.16	153.86	172.02	290.66	156.60	265.37	245.55
