


भूमि अधिग्रहण माह अप्रैल, 2014 (Land Acquisition for the month of April, 2014)

परियोजना विवरण Project Description		कुल क्षेत्र Total Scope			20 A		20 E		20 F		Amount (in Crs.)	
		Length (Km.)	Govt. Land	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Award	Disbursement
पश्चिमी कोरीडोर Western Corridor												
Phase-I रेवाड़ी-वडोदरा Rewari-Vadodara	हरियाणा Haryana	81	26	234	81	234	81	234	76	234	243	227
	राजस्थाना Rajasthan	543	429	1829	543	1829	543	1829	543	1829	282	251
	गुजरात Gujarat	307	170	1545	307	1545	307	1509	293	1442	713	496
कुल Total		930	625	3608	930	3608	930	3572	912	3504	1237	974
Phase-II वडोदरा-जेएनपीटी एवं रेवाड़ी -दादरी Vadodara- JNPT & Rewari- Dadri	गुजरात Gujarat	245	183	868	245	868	245	867	236	817	689	527
	महाराष्ट्र Maharashtra	183	147	442	183	442	183	442	164	438	510	161
	हरियाणा Haryana	111	8	745	111	745	95	665	86	651	1033	892
	राजस्थान Rajasthan	16	18	95	16	95	16	95	16	90	114	123
	उत्तर प्रदेश Uttar Pradesh	14	60	102	14	102	14	102	13	99	217	156
Total		569	417	2252	569	2252	553	2172	515	2095	2563	1859
Total of WDFC		1499	1043	5860	1499	5860	1483	5744	1427	5600	3800	2833

Phase-I Rewari-Vadodara

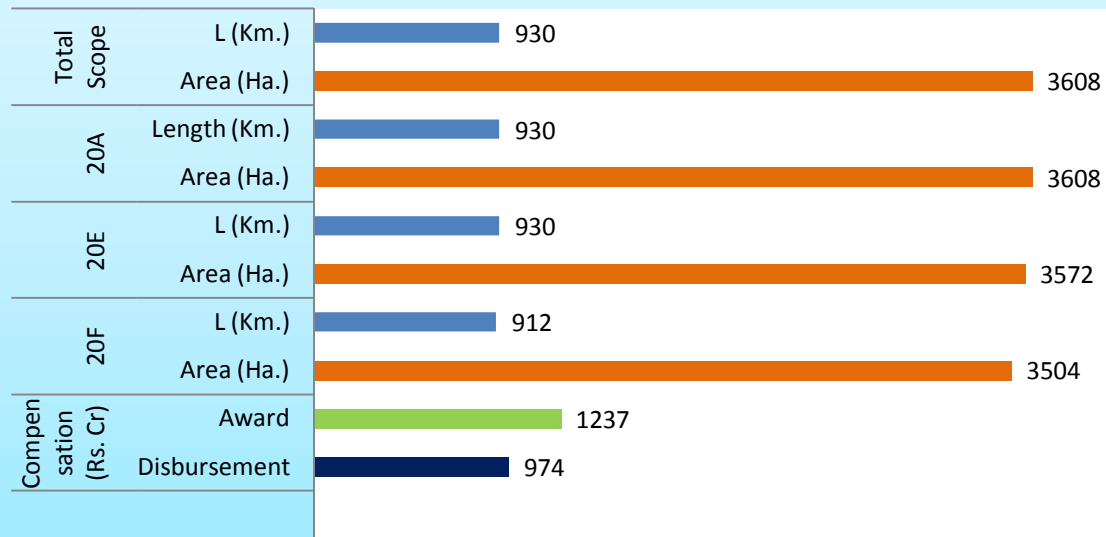

Phase-II - - Vadodara-JNPT & Rewari-Dadri

