


पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - II (भूमि अधिग्रहण प्रगति)
WDFC – PHASE – II (Land Acquisition Progress)

	(Kms)	22	52	60	37	72	34	39
Area (Ha.)		133	328	211	65	77	68	78
20A (Ha.)		133	328	211	65	77	68	78
20E (Ha.)		133	328	211	65	77	68	78
20F (Ha.)		133	328	199	62	66	32	15
Award Declared (Cr.)		5	140	569	49	39	159	5
Disbursed (Cr.)		5	119	425	33	35	122	7
Land Taken over (Ha.)		133	279	149	42	59	25	0

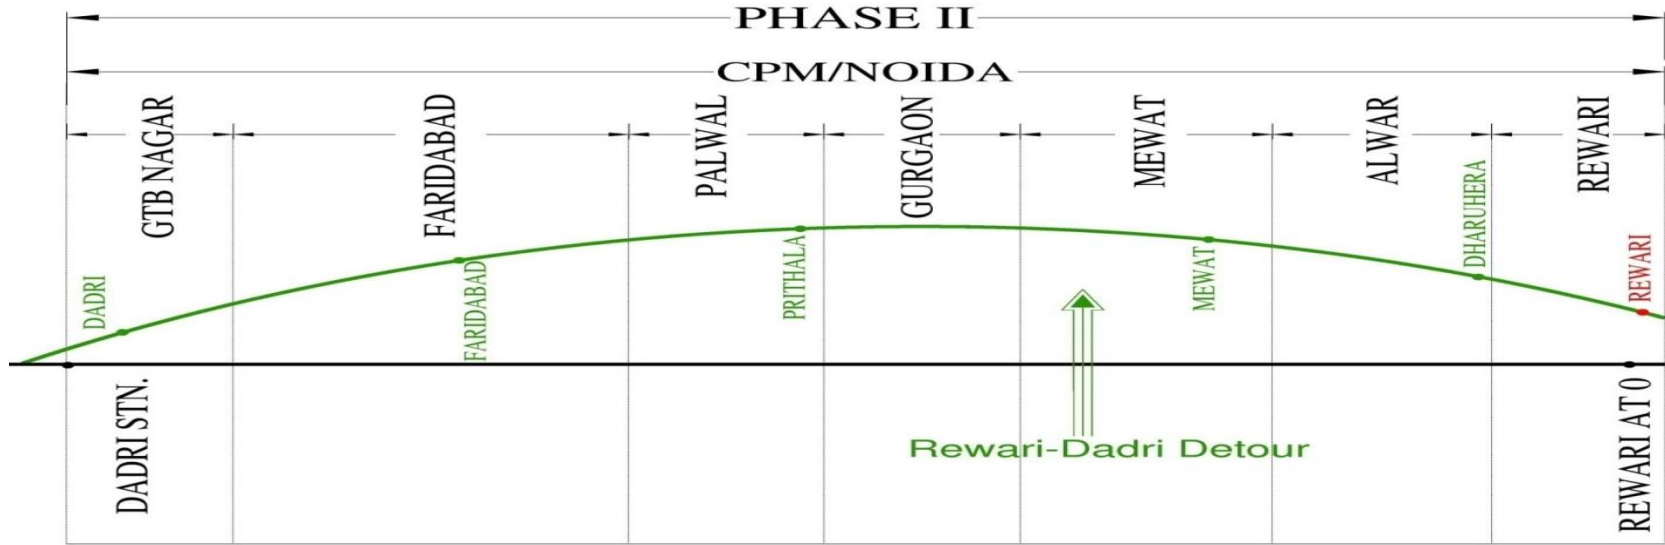

पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - II (भूमि अधिग्रहण प्रगति)

WDFC – PHASE – II (Land Acquisition Progress)

	(Kms)	19	28	15	12	20	16	20
	Area (Ha.)	175	207	127	77	163	132	145
20A (Ha.)		175	207	127	77	163	132	145
20E (Ha.)		175	207	127	77	163	132	145
20F (Ha.)		158	207	127	77	163	115	145
Award Declared (Cr.)		471	503	307	189	263	258	179
Disbursed (Cr.)		364	468	280	185	236	250	169
Land Taken over (Ha.)		122	-	-	-	-	-	137
