


पश्चिमी डेडीकेड फ्रेट कोरीडोर- फेज - II (भूमि अधिग्रहण प्रगति)

WDFC – PHASE – II (Land Acquisition Progress)

	(Kms)	22	53	60	37	72	138	45
Area (Ha.)		135	395	269	81	96	401	59
20A (Ha.)		115	288	205	81	96	398	44
20E (Ha.)		115	279	180	53	91	398	44
20F (Ha.)		115	253	167	36	63	398	44
Award Declared (Cr.)		0	120	456	34	35	490	5
Disbursed (Cr.)		0	103	364	29	26	167	3
Land Taken over (Ha.)		-	217	133	31	47	136	0

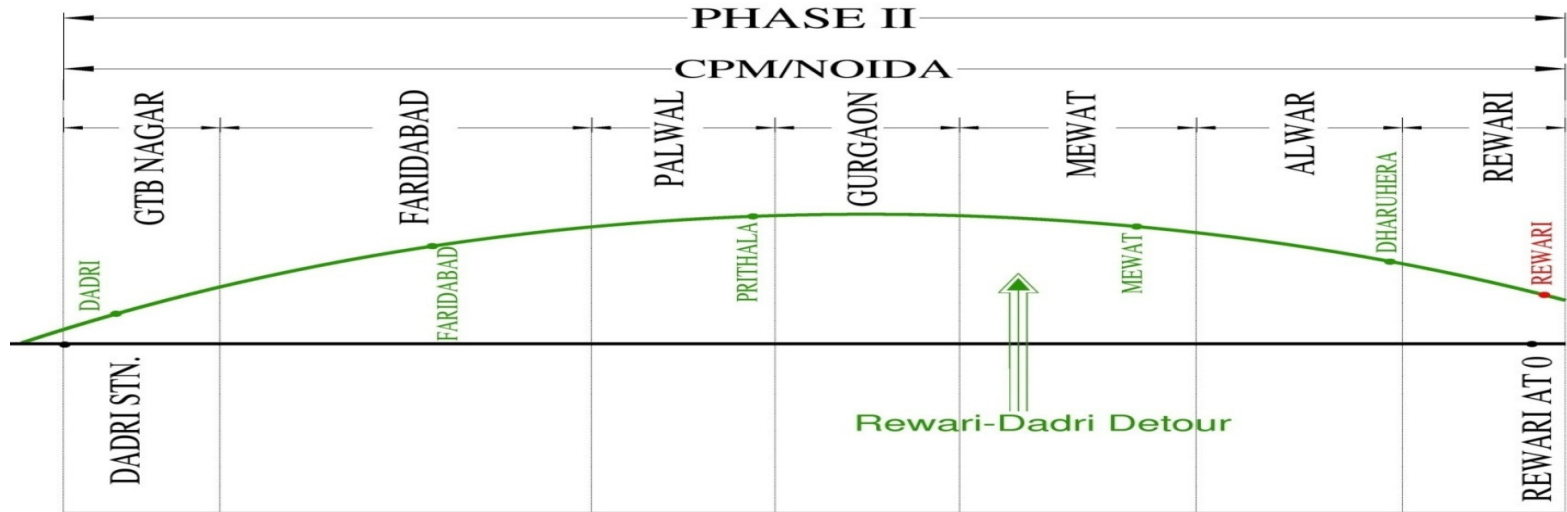

पश्चिमी डेडीकेटेड फ्रेट कोरीडोर- फेज - II (भूमि अधिग्रहण प्रगति)

WDFC – PHASE – II (Land Acquisition Progress)

	(Kms)	19	28	15	12	20	16	20
	Area (Ha.)	172	214	130	89	163	128	148
20A (Ha.)		172	214	130	89	163	128	148
20E (Ha.)		104	168	129	79	161	81	148
20F (Ha.)		104	168	129	79	127	81	148
Award Declared (Cr.)		216	369	303	196	166	120	183
Disbursed (Cr.)		161	339	235	163	153	91	130
Land Taken over (Ha.)		78	-	-	-	-	-	105
