


### WDFC – PHASE – II (Land Acquisition Progress June 2018)

	(Kms)	22	52	60	37	72	34	39
	Area (Ha.)	133	328	209	65	77	68	78
20A (Ha.)		133	328	209	65	77	68	78
20E (Ha.)		133	328	209	65	77	68	78
20F (Ha.)		133	328	209	63	73	57	67
Award Declared (Cr.)		7	172	599	51	55	438	38
Disbursed (Cr.)		7	144	578	46	41	319	37
Land Taken over PAP (Ha.)		147	321	180	37	52	41	8

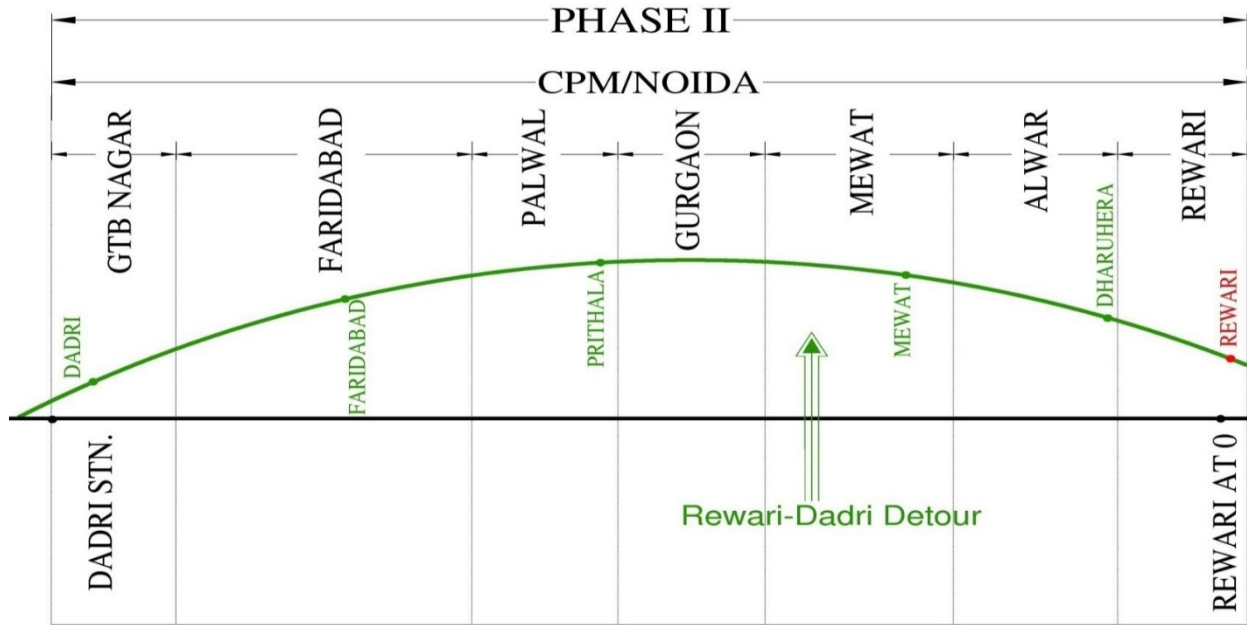

WDFC – PHASE – II (Land Acquisition Progress June 2018)								
	(Kms)	19	28	15	12	20	16	20
	Area (Ha.)	175	207	127	77	163	132	145
20A (Ha.)	175	207	127	77	163	132	145	
20E (Ha.)	175	207	127	77	163	132	145	
20F (Ha.)	175	207	127	77	163	132	145	
Award Declared (Crs.)	564	508	323	196	274	264	191	
Disbursed (Crs.)	559	485	309	187	244	254	186	
Land Taken over PAP (Ha.)	75	197	122	75	152	74	141	
