


		WDFC - PHASE – I (Land Acquisition Progress June 2018)						
Scope	(Kms)	34	46	2	85	5	101	98
	Area (Ha.)	154	98	7	330	6	443	349
20A (Ha.)		154	98	7	330	6	443	349
20E (Ha.)		154	98	7	330	6	443	349
20F (Ha.)		154	98	7	330	6	439	349
Award Declared (Crs.)		158	88	3	46	0	32	125
Disbursed (Crs.)		155	88	2	46	0	31	95
Land Taken over PAP (Ha.)		149	98	7	298	6	349	274

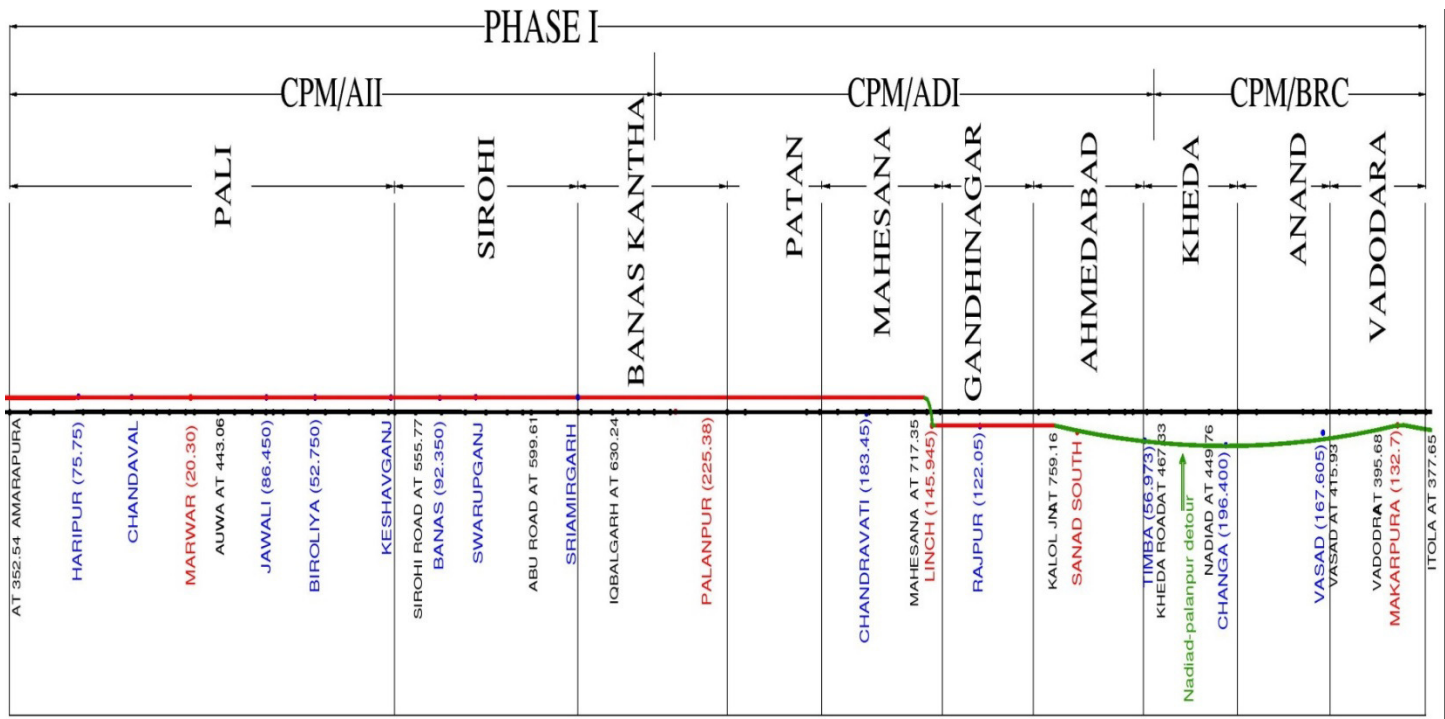

WDFC – PHASE – I (Land Acquisition Progress June 2018)

	(Kms)	196	65	77	12	64	30	35	29	43	32
	Area (Ha.)	546	142	231	16	166	189	312	166	291	270
20A (Ha.)		546	142	231	16	166	189	312	166	291	270
20E (Ha.)		546	142	231	16	166	189	312	166	291	270
20F (Ha.)		546	142	231	16	166	189	312	166	290	270
Award Declared (Cr.)		20	35	87	4	112	112	121	12	108	169
Disbursed (Cr.)		20	34	73	4	101	106	86	12	99	166
Land Taken over PAP (Ha.)		317	87	190	14	153	169	276	156	265	245
