


**LEGEND**  
 IR TRACK  
 DFC ALIGNMENT (PARALLEL)  
 DFC ALIGNMENT (DETOUR)  
 JUNCTION STATIONS  
 X-ING STATIONS  
 IR STATIONS

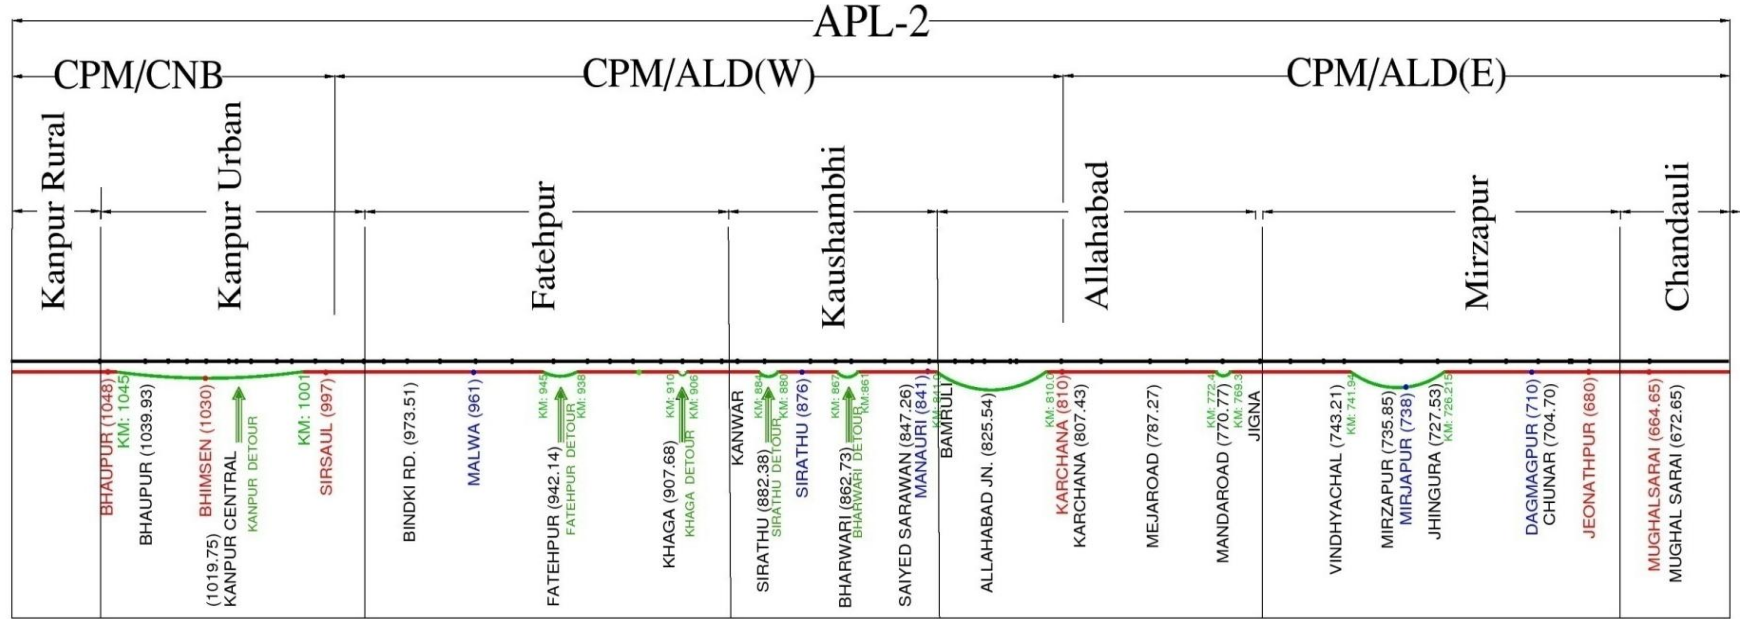

## पूर्वी डेडीकेटेड फ्रेट कोरीडोर - एपील -2 ( भूमि अधिग्रहण प्रगति )

### EDFC - APL – 2 (Land Acquisition Progress)

	( Kms)	6	63	104	47	84	92	4
	Area (Ha.)	16	238	168	125	446	546	15
20A (Ha.)		16	238	168	125	446	546	15
20E (Ha.)		16	235	167	125	446	544	15
20F (Ha.)		16	229	166	125	446	544	15
Award Declared (Crs.)		2	2	33	27	122	144	8
Disbursed (Crs.)		1	1	26	24	106	118	5
Land Taken over (Ha.)		10	147	131	110	388	446	9
