


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

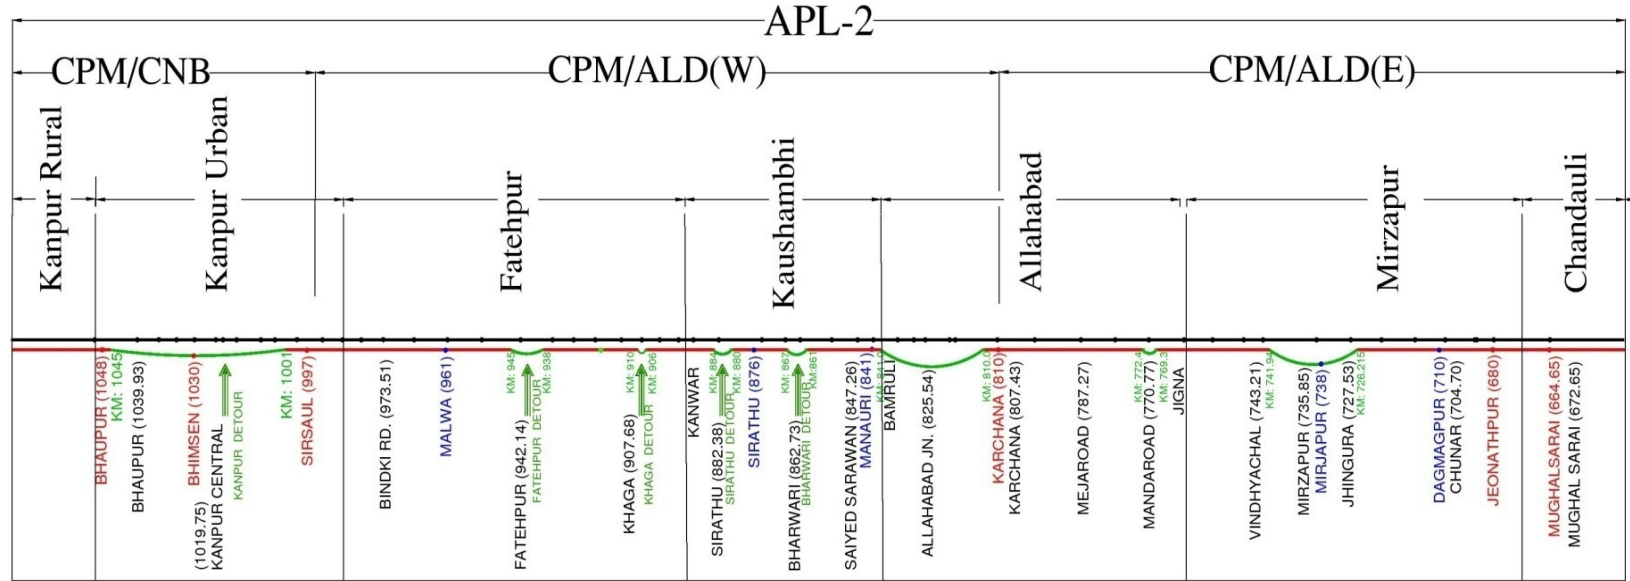

पूर्वी डेडीकेटेड फ्रेट कोरीडोर - एपील -2 (भूमि अधिग्रहण प्रगति)

EDFC - APL – 2 (Land Acquisition Progress)

	(Kms)	6	63	104	47	84	92	4
	Area (Ha.)	16	238	168	125	409	495	14
20A (Ha.)		16	235	167	125	409	483	14
20E (Ha.)		16	229	166	125	394	479	13
20F (Ha.)		16	229	166	125	394	456	12
Award Declared (Cr.)		99	99	33	27	121	119	5
Disbursed (Cr.)		89	89	24	22	96	87	5
Land Taken over (Ha.)		14	205	124	101	311	333	12
