


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

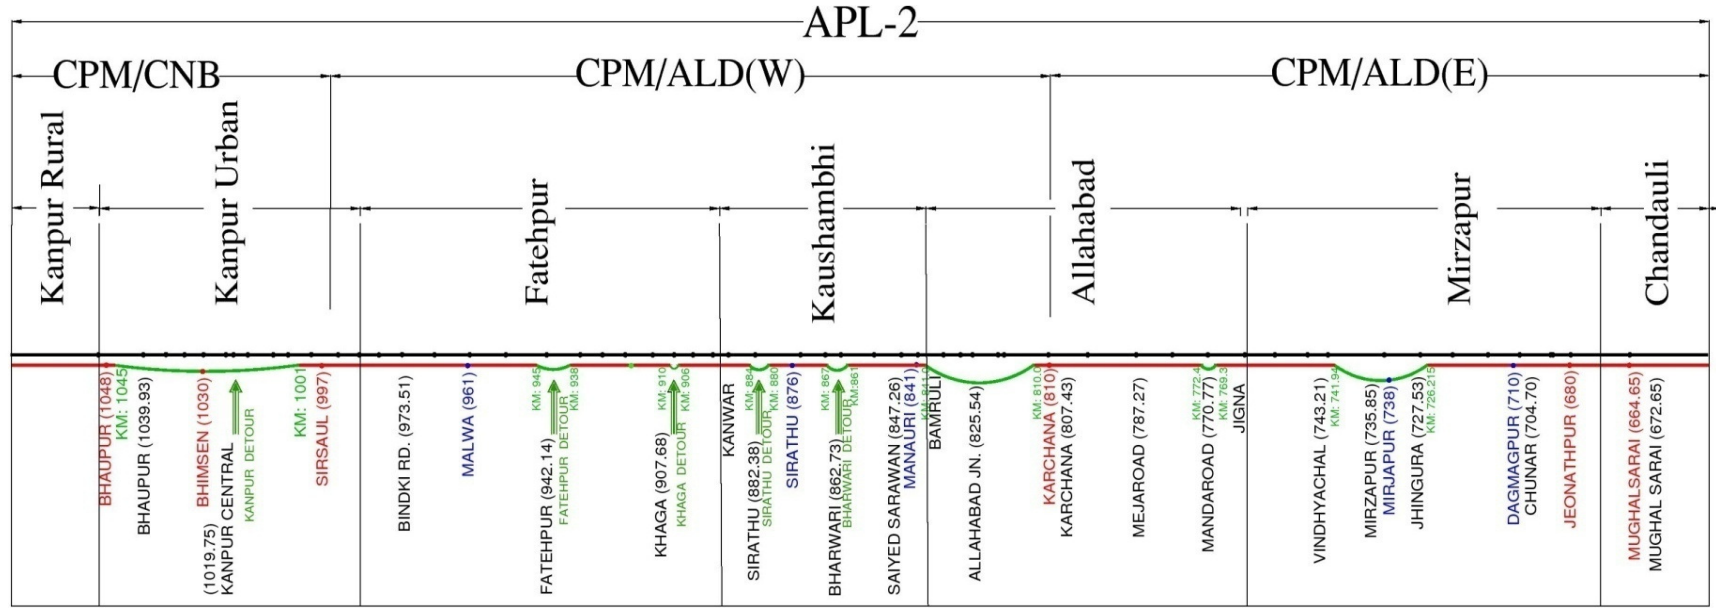

पूर्वी डेडीकेटेड फ्रेट कोरीडोर - एपल - 2 (भूमि अधिग्रहण प्रगति माह अप्रैल, 2014)

EDFC - APL – 2 (Land Acquisition Progress for the Month of April 2014)

| | (Kms) | 4 | 62 | 91 | 59 | 73 | 92 | 4 |
|-----------------------|------------|----|-----|-----|-----|-----|-----|----|
| | Area (Ha.) | 16 | 241 | 164 | 122 | 391 | 442 | 15 |
| 20A (Ha.) | | 16 | 241 | 164 | 122 | 391 | 442 | 15 |
| 20E (Ha.) | | 16 | 241 | 164 | 122 | 391 | 442 | 15 |
| 20F (Ha.) | | 16 | 241 | 164 | 122 | 391 | 415 | 15 |
| Award Declared (Cr.) | | 3 | 93 | 30 | 27 | 105 | 115 | 5 |
| Disbursed (Cr.) | | 3 | 82 | 24 | 21 | 90 | 82 | 5 |
| Land Taken over (Ha.) | | 14 | 213 | 131 | 93 | 334 | 295 | 15 |
