


LEGEND
 IR TRACK
 DFC ALIGNMENT (PARALLEL)
 DFC ALIGNMENT (DETOUR)
 JUNCTION STATIONS
 X-ING STATIONS
 IR STATIONS

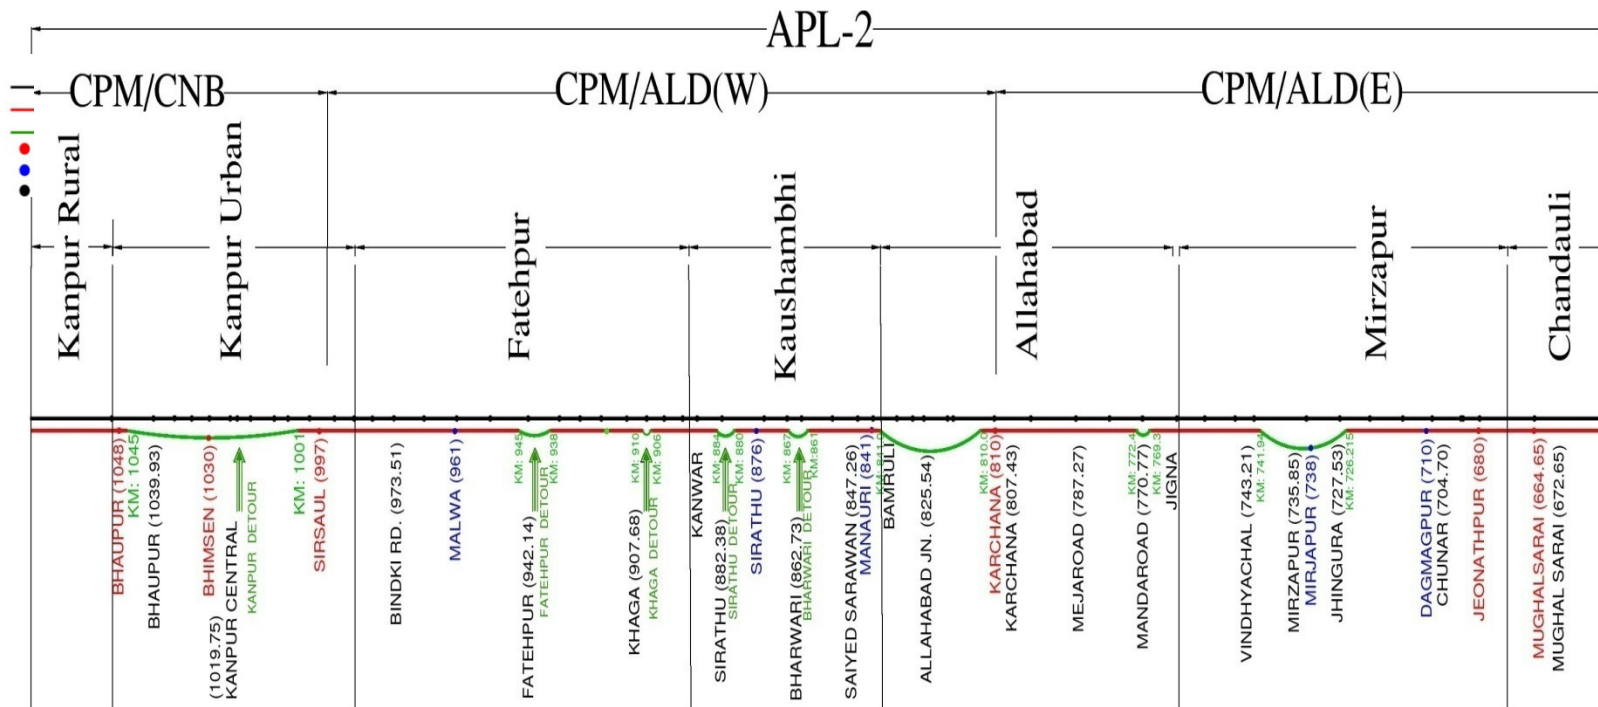

EDFC - APL – 2 (Land Acquisition Progress for the Month of June 2018)

	(Kms)	6	63	104	47	84	92	6
	Area (Ha.)	16	250	168	125	446	546	24
20A (Ha.)		16	250	168	125	446	546	24
20E (Ha.)		16	250	167	125	446	545	24
20F (Ha.)		16	250	166	125	446	544	23
Award Declared (Crs.)		4	137	41	27	152	203	23
Disbursed (Crs.)		4	129	35	25	115	152	9
Land Taken over (Ha.)		14	203	136	111	362	496	21
