


LEGEND

IR TRACK
 DFC ALIGNMENT (PARALLEL)
 DFC ALIGNMENT (DETOUR)
 JUNCTION STATIONS
 X-ING STATIONS
 IR STATIONS

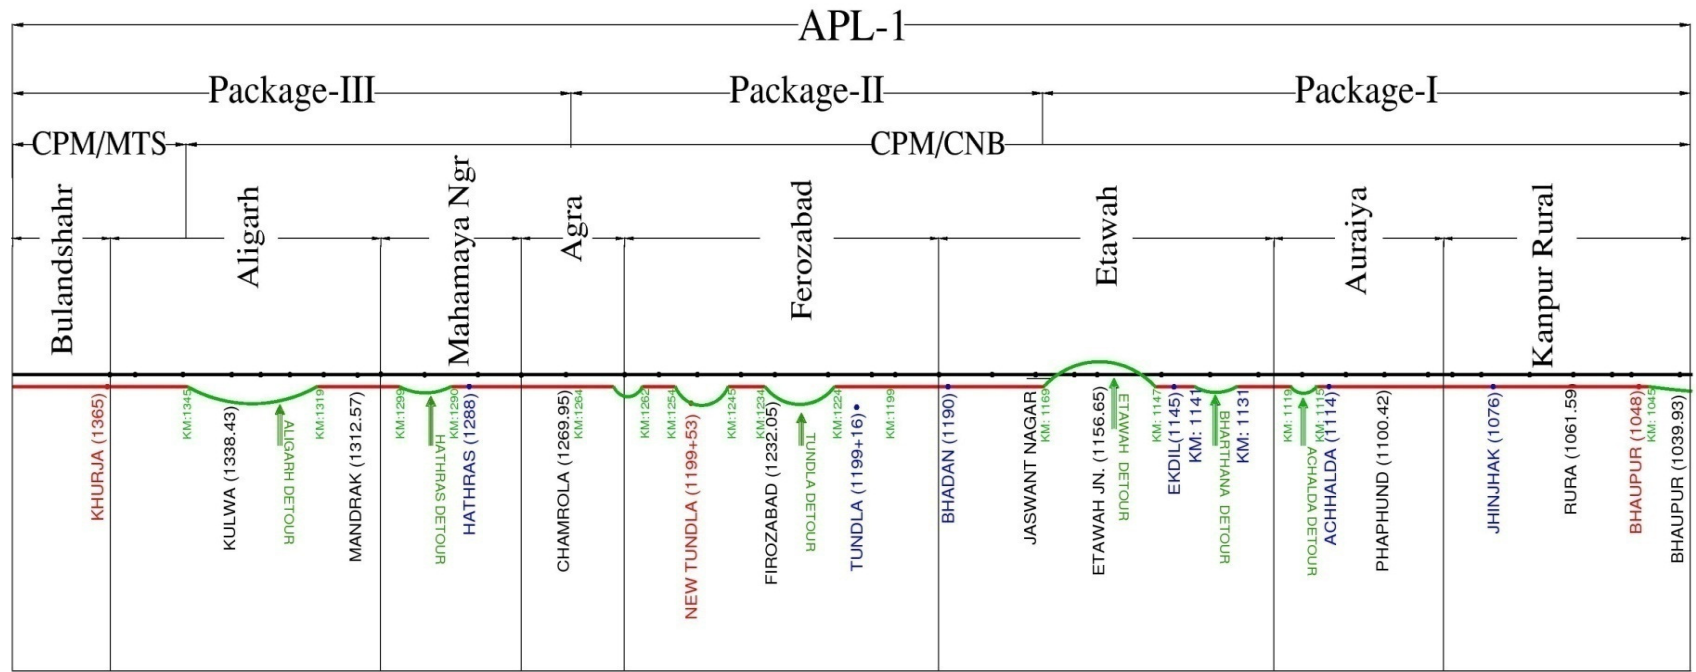

पूर्वी डेडीकेटेड फ्रेट कोरीडोर - एएल-1 (भूमि अधिग्रहण प्रगति माह अप्रैल, 2014)

EDFC - APL-1 (Land Acquisition Progress for the Month of April 2014)

| क्षेत्र Scope | (Kms) | 15 | 45 | 42 | 24 | 66 | 64 | 33 | 55 |
|---------------------------|---------------|----------|----------|----------|----------|----------|----------|----------|-----|
| | Area (Ha.) | 59 | 233 | 170 | 78 | 234 | 293 | 109 | 144 |
| 20A (Ha.) | 59 | 233 | 170 | 78 | 234 | 293 | 109 | 144 | |
| 20E (Ha.) | 59 | 233 | 170 | 78 | 234 | 293 | 109 | 144 | |
| 20F (Ha.) | 59 | 233 | 170 | 78 | 229 | 293 | 109 | 144 | |
| Award Declared (Cr.) | 26 | 160 | 94 | 51 | 121 | 60 | 13 | 14 | |
| Disbursed (Cr.) | 16 | 152 | 91 | 46 | 113 | 48 | 10 | 12 | |
| Land Taken over (Ha.) | 37 | 222 | 164 | 70 | 214 | 231 | 85 | 122 | |
| Arbitration Cases No. | - | 1 | 1 | - | - | 49 | 2 | 2 | |
| Last Date of 20E Notf. | 20.04.11 | 26.02.10 | 15.07.10 | 03.11.11 | 03.11.11 | 22.06.11 | 22.06.11 | 18.11.11 | |
