


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

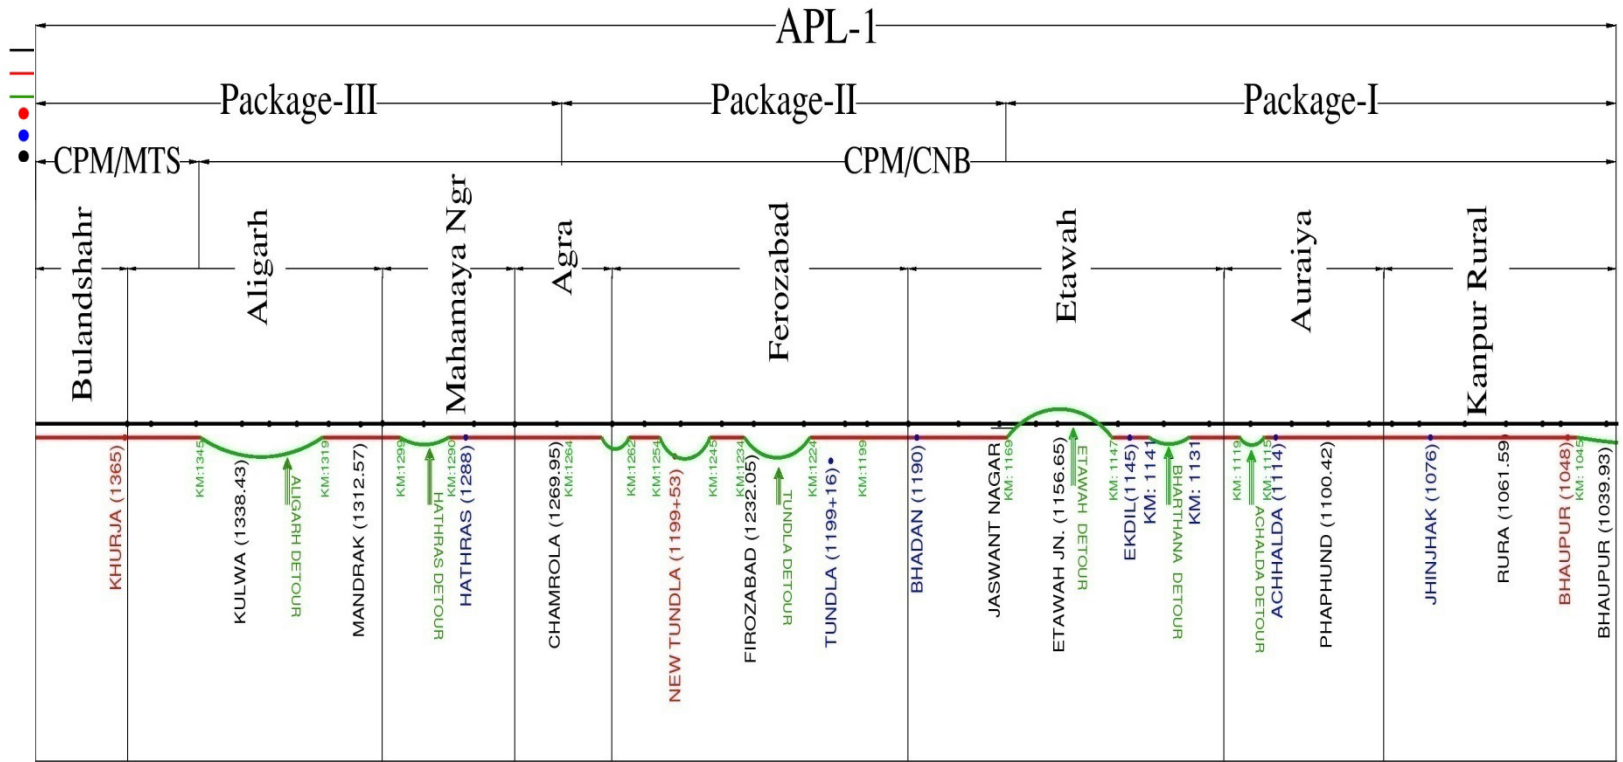

EDFC - APL-1 (Land Acquisition Progress for the Month of June 2018)

Scope	(Kms)	15	45	42	24	66	64	33	55
	Area (Ha.)	47	254	180	104	247	297	113	164
20A (Ha.)	47	254	180	104	247	297	113	164	
20E (Ha.)	48	252	179	104	247	297	110	164	
20F (Ha.)	47	251	175	105	247	297	110	164	
Award Declared (Cr.)	22	202	101	76	125	148	36	43	
Disbursed (Cr.)	28	197	96	68	125	130	25	37	
Land Taken over (Ha.)	38	271	143	91	224	272	83	143	
