


Land Acquisition June 2018

Section Wise Progress of Land Acquisition for the month of June 2018		Total Scope				20 A		20 E		20 F		Amount (in Crs.)	
		Length (Km.)	Pvt. Land	Govt. Land	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Award	Disbursement
Western Corridor													
Phase-I Rewari- Vadodara	Haryana	81	252	1	252	81	252	81	252	81	252	259	256
	Rajasthan	552	1349	475	1824	552	1824	552	1824	552	1820	311	275
	Gujarat	321	1469	171	1640	321	1640	321	1640	321	1639	895	805
Total		954	3070	647	3716	954	3716	954	3716	954	3711	1465	1337
Phase-II Vadodara- JNPT & Rewari- Dadri	Gujarat	244	734	79	813	244	813	244	813	246	806	957	877
	Maharashtra	177	264	181	444	177	444	177	444	147	406	1134	854
	Haryana	96	713	6	719	96	719	96	719	96	719	1521	1432
	Rajasthan	16	88	44	132	16	132	16	132	16	132	267	257
	Uttar Pradesh	19	94	82	175	19	175	19	175	19	175	566	560
Total		551	1893	391	2283	551	2283	551	2283	524	2238	4445	3980
Total of WDFC		1505	4962	1037	6000	1505	6000	1505	5999	1477	5949	5910	5317

Phase-I Rewari-Vadodara

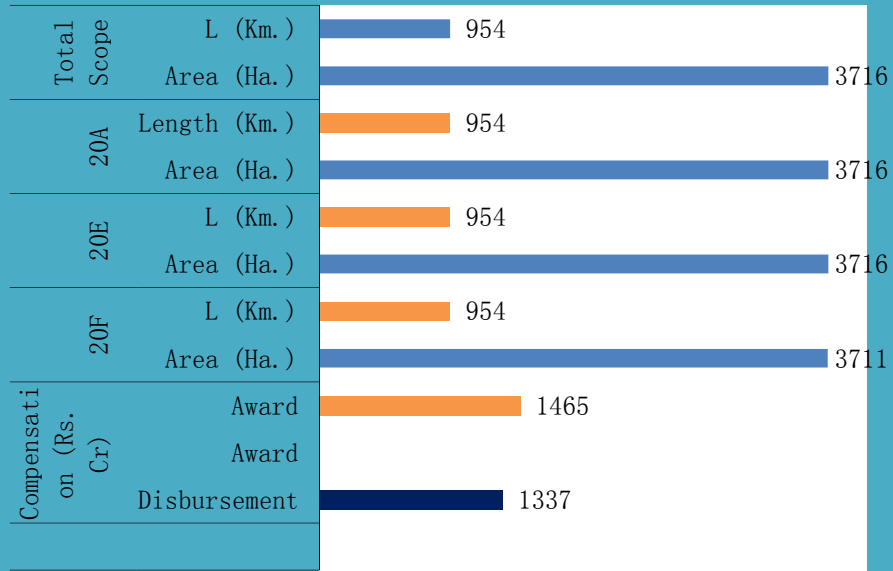

Phase-II Vadodara-JNPT & Rewari-Dadri

