


**LEGEND**

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

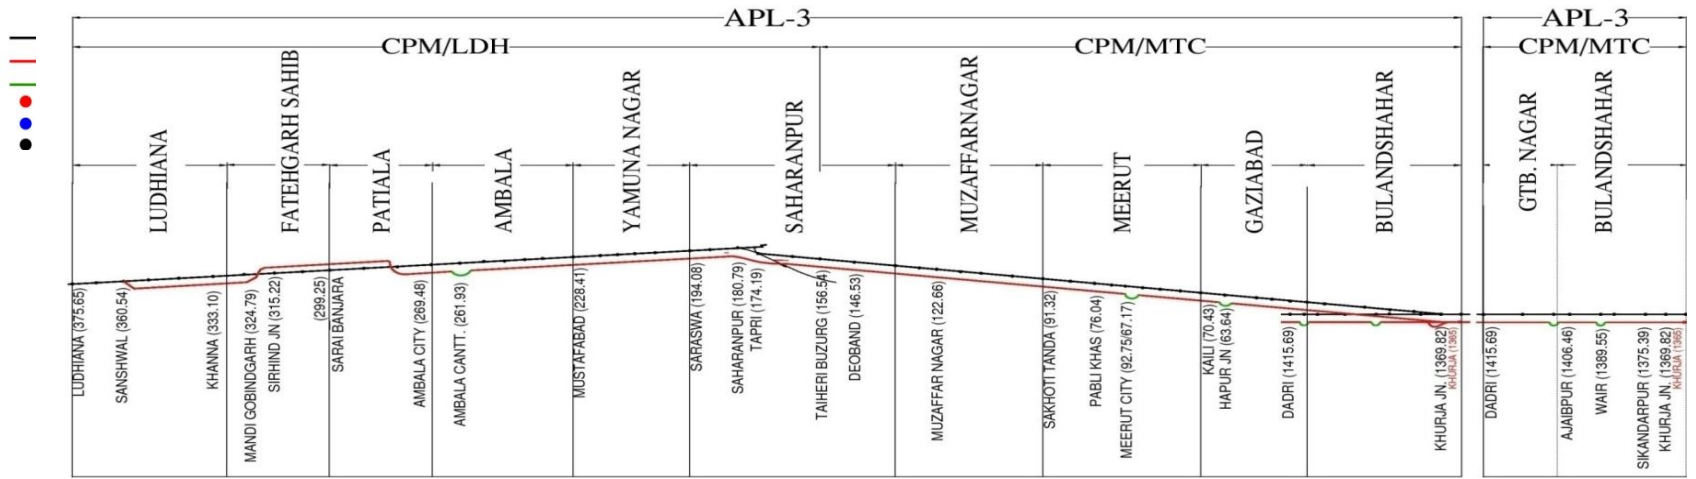

**पूर्वी डेडीकेटेड फ्रेट कोरीडोर - एपीएल-3 (भूमि अधिग्रहण प्रगति)**

**EDFC - APL-3 (Land Acquisition Progress)**

	( Kms)	33	27	27	43	29	35	44	42	14	48	19	28
	Area (Ha.)	70	115	76	62	10	114	172	223	186	36	85	132
20A (Ha.)		70	115	76	62	10	114	172	223	186	36	85	132
20E (Ha.)		70	115	76	62	10	103	131	189	157	30	79	131
20F (Ha.)		70	115	76	46	10	58	14	30	15	30	56	129
Award Declared (Cr.)		322	348	219	35	10	24	15	42	7	54	75	107
Disbursed (Cr.)		289	323	208	32	7	17	13	40	6	17	26	45
Land Taken over (Ha.)		63	107	72	42	8	41	13	28	12	9	19	54
