


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

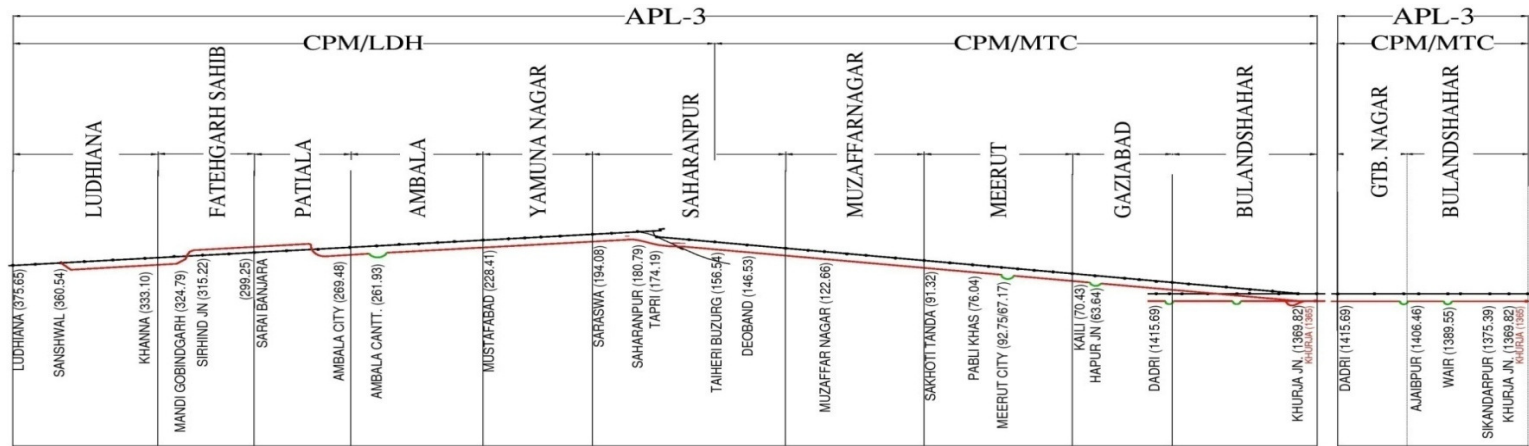

पूर्वी डेडीकेटेड फ्रेट कोरीडोर - एपीएल-3 (भूमि अधिग्रहण प्रगति)

EDFC - APL-3 (Land Acquisition Progress)

	(Kms)	33	27	27	43	29	35	44	42	14	48	19	28
	Area (Ha.)	70	115	78	64	12	118	178	234	206	36	90	131
20A (Ha.)		70	115	78	64	12	25	14	40	203	30	84	124
20E (Ha.)		70	115	78	64	12	25	14	30	12	30	79	111
20F (Ha.)		70	115	78	43	9	19	14	30	12	30	37	111
Award Declared (Cr.)		355	346	216	27	8	16	15	41	7	36	37	52
Disbursed (Cr.)		285	313	200	24	7	12	12	39	5	8	18	35
Land Taken over (Ha.)		56	104	72	38	8	14	12	28	8	7	18	76
