


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

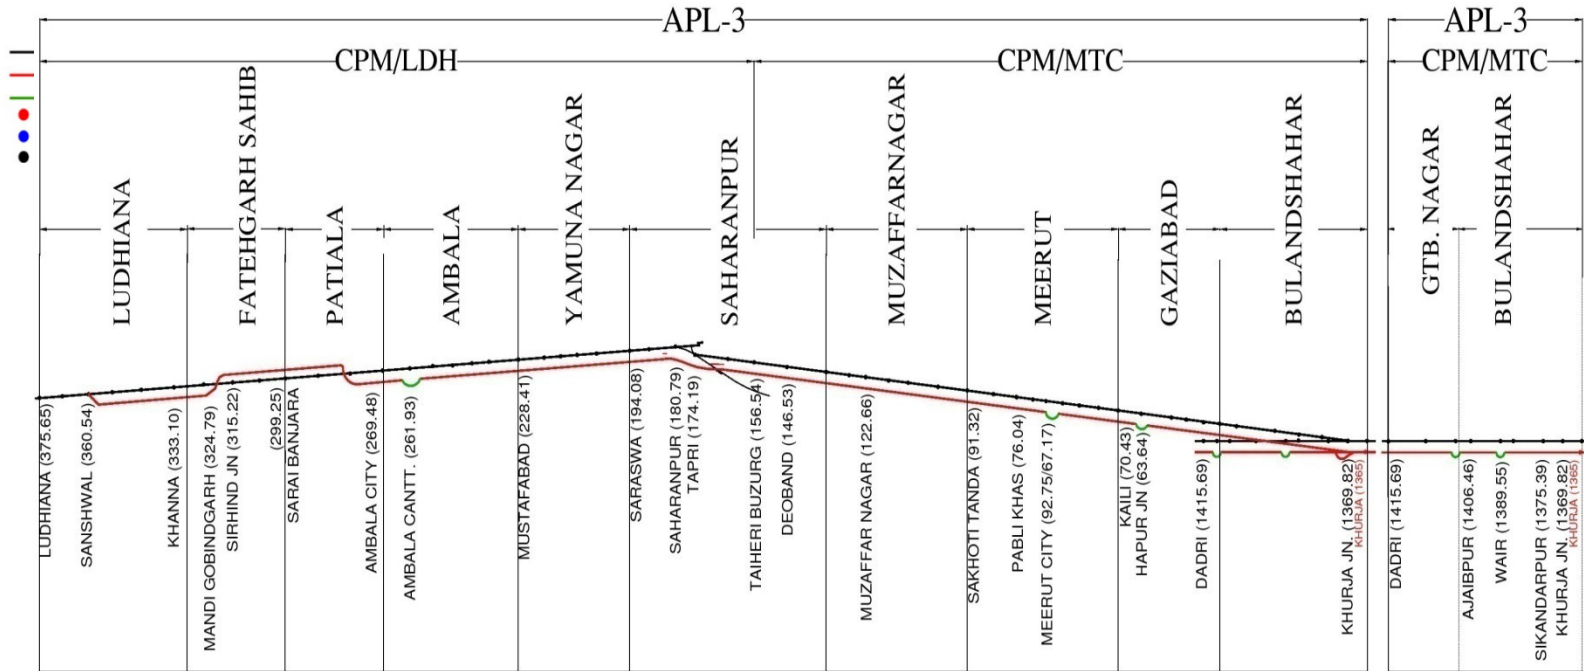

EDFC - APL-3 (Land Acquisition Progress for the Month of June 2018)

	(Kms)	33	27	27	43	29	67	44	42	40	48	19	28
	Area (Ha.)	70	115	76	62	10	162	172	223	186	36	85	133
20A (Ha.)		70	115	76	62	10	162	172	223	186	36	85	133
20E (Ha.)		70	115	76	62	10	157	155	191	177	30	79	133
20F (Ha.)		70	115	76	62	10	157	155	191	177	30	56	133
Award Declared (Cr.)		318	348	268	37	10	217	470	791	623	55	75	111
Disbursed (Cr.)		294	332	257	32	7	193	372	579	520	32	209	97
Land Taken over (Ha.)		68	114	75	46	9	137	120	140	140	18	39	104
