


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

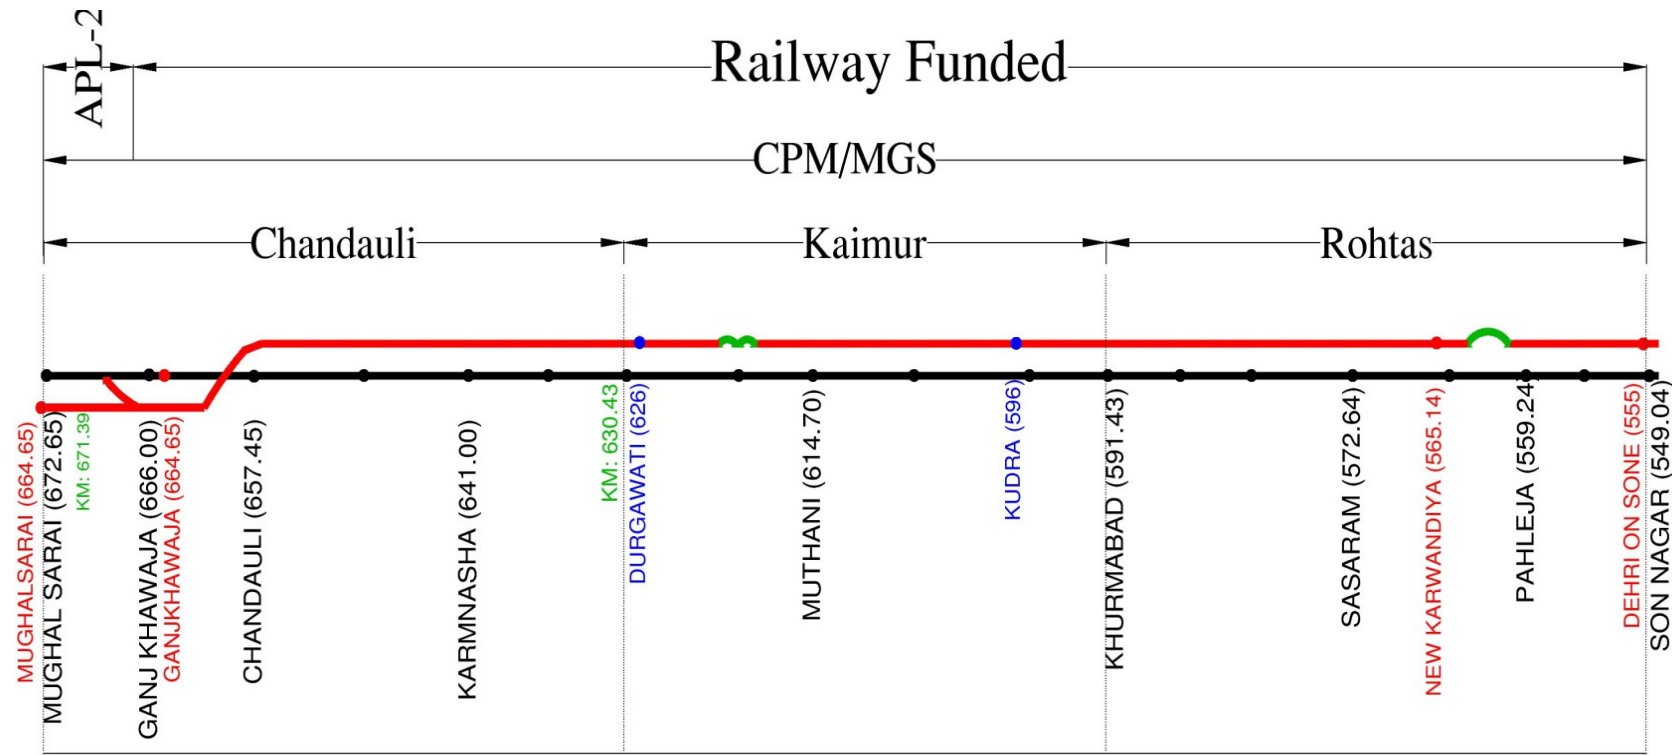

रेलवे फंडेड (भूमि अधिग्रहण प्रगति माह अप्रैल, 2014)

RAILWAY FUNDED (Land Acquisition Progress for the Month of April 2014)

Scope	(Kms)	34	49	43
	Area (Ha.)	61	115	153
20A (Ha.)	61	115	153	
20E (Ha.)	56	112	151	
20F (Ha.)	51	111	148	
Award Declared (Cr.)	27	100	108	
Disbursed (Cr.)	18	72	81	
Land Taken over (Ha.)	35	80	111	
Arbitration Cases No.		12	1	
Last Date of 20E Notf.	16.12.11	05.05.11	15.12.11	
