


WDFC - PHASE – I (Land Acquisition Progress November 2018)								
Scope	(
	Kms)	34.49	46.12	2.34	84.83	4.63	101.08	98.11
	Area (Ha.)	154.09	98.36	7.44	330.15	6.12	443.08	348.62
20A (Ha.)		154.09	98.36	7.44	330.15	6.12	443.08	348.62
20E (Ha.)		154.09	98.36	7.44	330.15	6.12	443.08	348.62
20F (Ha.)		154.09	98.36	7.44	330.15	6.12	442.76	348.62
Award Declared (Crs.)		163.97	95.17	3.52	60.16	0.50	46.25	138.00
Disbursed (Crs.)		161.08	95.17	2.82	55.51	0.49	45.76	121.07
Land Taken over PAP (Ha.)		149.28	97.76	7.20	297.73	5.84	349.13	273.69

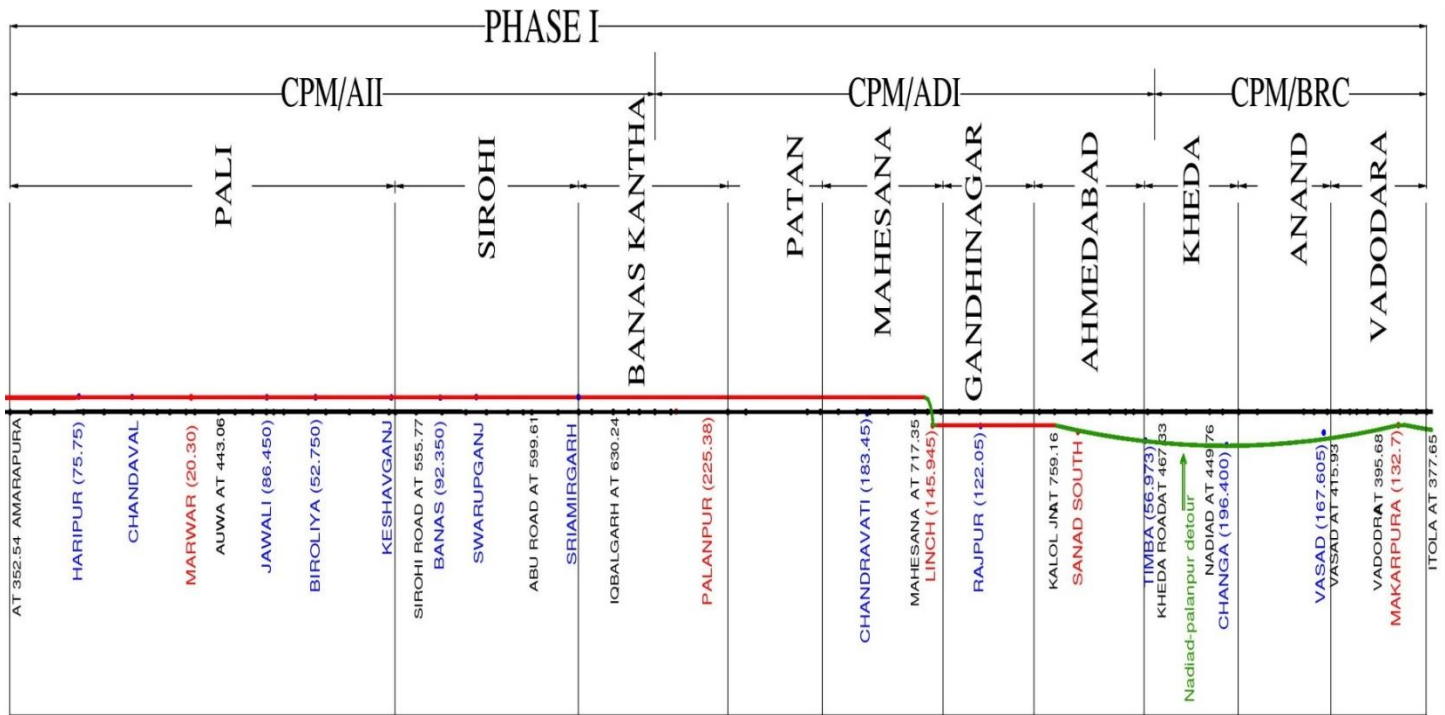

WDFC – PHASE – I (Land Acquisition Progress November 2018)

	(Kms)	195.56	65.02	76.90	11.52	64.10	29.87	35.22	28.74	43.40	31.52
	Area (Ha.)	546.36	141.99	231.31	16.15	166.00	188.93	311.51	165.79	290.76	269.73
20A (Ha.)		546.36	141.99	231.31	16.15	166.00	188.93	311.51	165.79	290.76	269.73
20E (Ha.)		546.36	141.99	231.11	16.15	166.00	188.52	311.51	165.79	290.76	269.73
20F (Ha.)		546.36	141.99	231.11	16.15	166.00	188.52	311.51	165.79	289.98	269.73
Award Declared (Crs.)		32.30	40.28	105.16	4.74	117.50	118.91	127.36	17.04	119.92	296.97
Disbursed (Crs.)		31.13	39.90	97.66	4.68	107.90	115.27	88.88	15.23	109.02	293.60
Land Taken over PAP(Ha.)		316.75	87.47	191.87	13.84	153.27	168.99	275.02	155.89	265.37	245.13
