


LEGEND
 IR TRACK
 DFC ALIGNMENT (PARALLEL)
 DFC ALIGNMENT (DETOUR)
 JUNCTION STATIONS
 X-ING STATIONS
 IR STATIONS

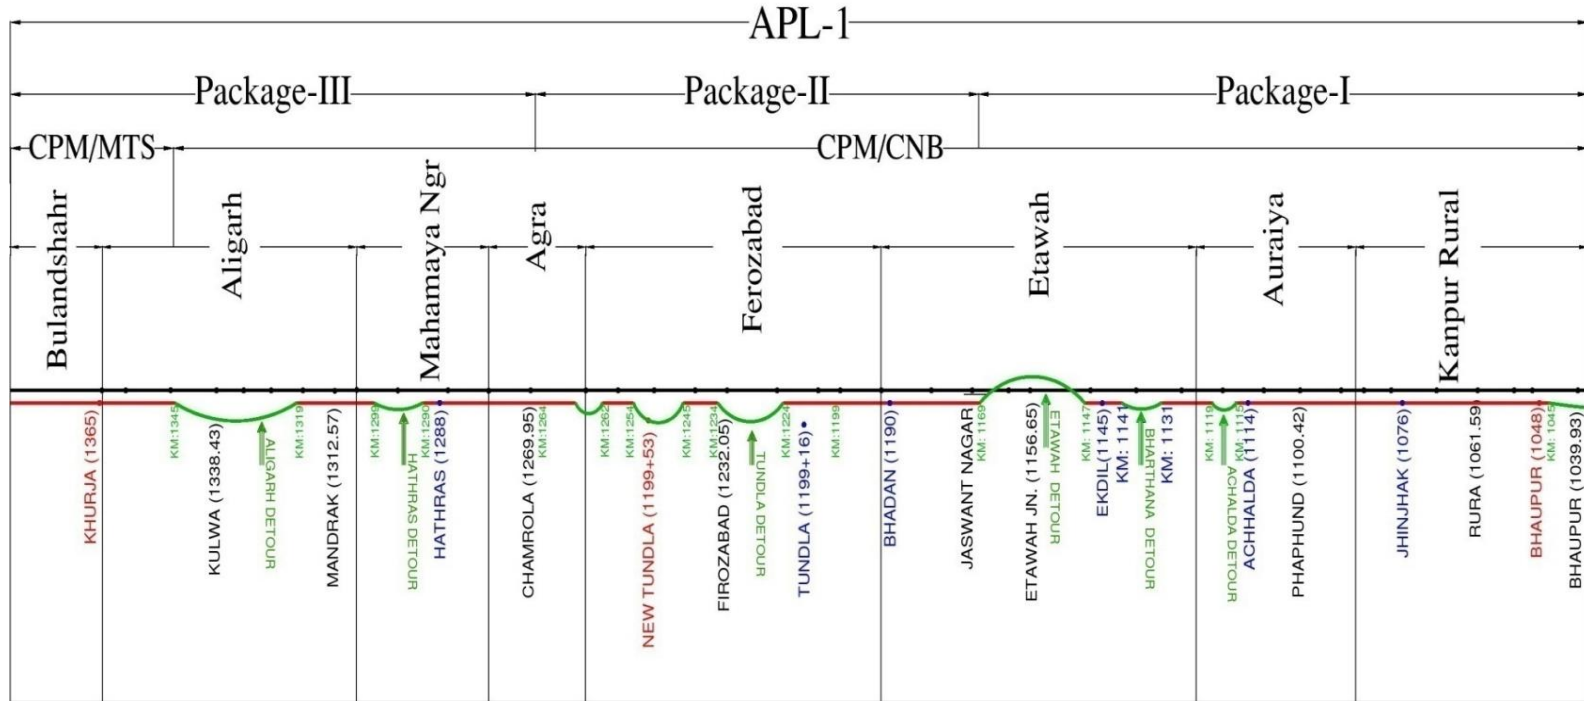

EDFC - APL-1 (Land Acquisition Progress for the Month of December 2020)

Districts		Bulandshahr	Aligarh	Mahamaya Nagar	Agra	Ferozabad	Etawah	Auraiya	Kanpur Rural
Scope	(Kms)	15	45	42	24	66	64	33	55
	Area (Ha.)	47	254	180	104	247	297	113	164
20A (Ha.)		47	254	180	104	247	297	113	164
20E (Ha.)		47	254	180	104	247	297	113	164
20F (Ha.)		47	254	180	104	247	297	113	164
Award Declared (Crns.)		46	217	110	84	140	168	46	63
Disbursed (Crns.)		36	211	109	79	139	164	43	61
Land Taken over (Ha.)		47	254	180	104	247	297	113	164
