


**LEGEND**

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS



EDFC - APL – 2 (Land Acquisition Progress for the Month of December 2020)								
District	Kanpur Rural	Kanpur Urban	Fatehpur	Kaushambhi	Allahabad	Mirzapur	Chandauli	
Scope	( Kms)	6	63	104	47	84	92	24
	Area (Ha.)	16	250	168	125	416	502	23
20A (Ha.)		16	250	168	125	416	502	23
20E (Ha.)		16	250	168	125	416	502	23
20F (Ha.)		16	250	168	125	416	502	23
Award Declared (Cr.)		161		58	62	187	234	26
Disbursed (Cr.)		4	155	52	60	153	185	13
Land Taken over (Ha.)		16	250	168	125	416	490	23

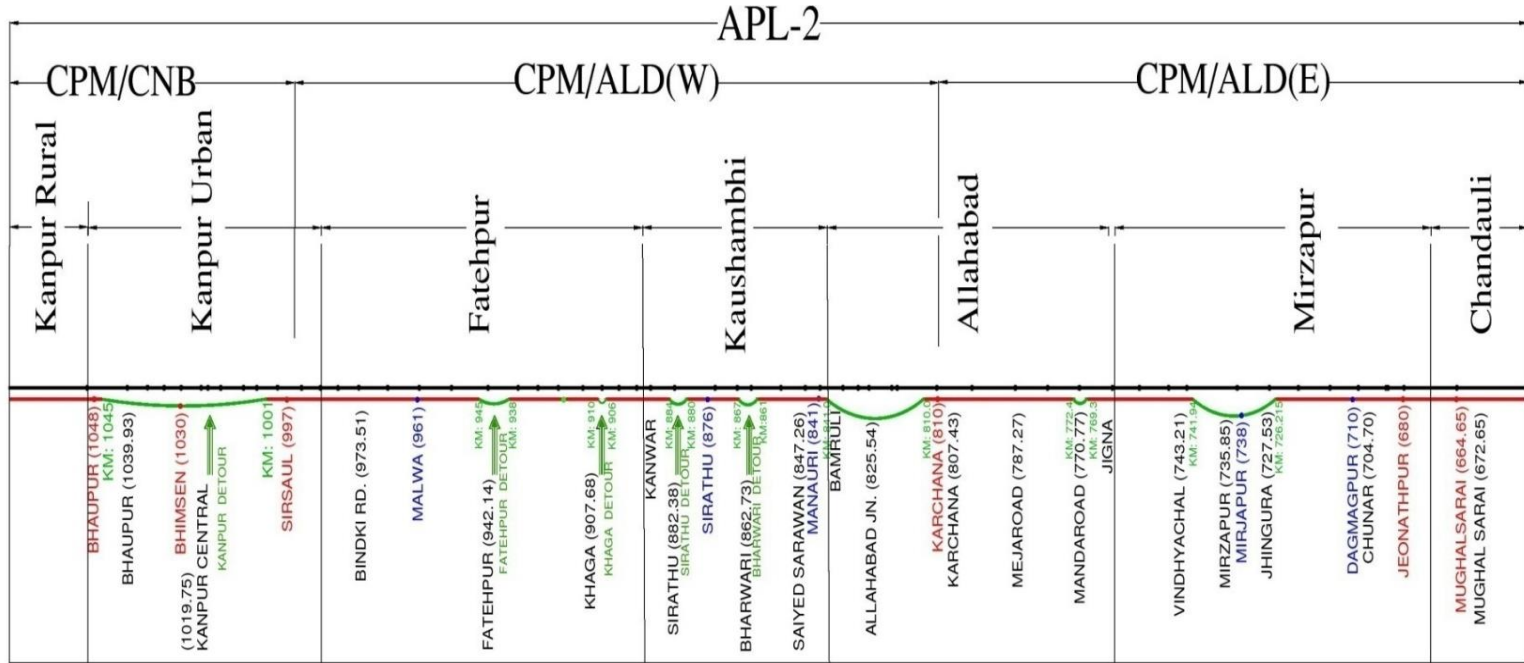
