


LEGEND
 IR TRACK
 DFC ALIGNMENT (PARALLEL)
 DFC ALIGNMENT (DETOUR)
 JUNCTION STATIONS
 X-ING STATIONS
 IR STATIONS

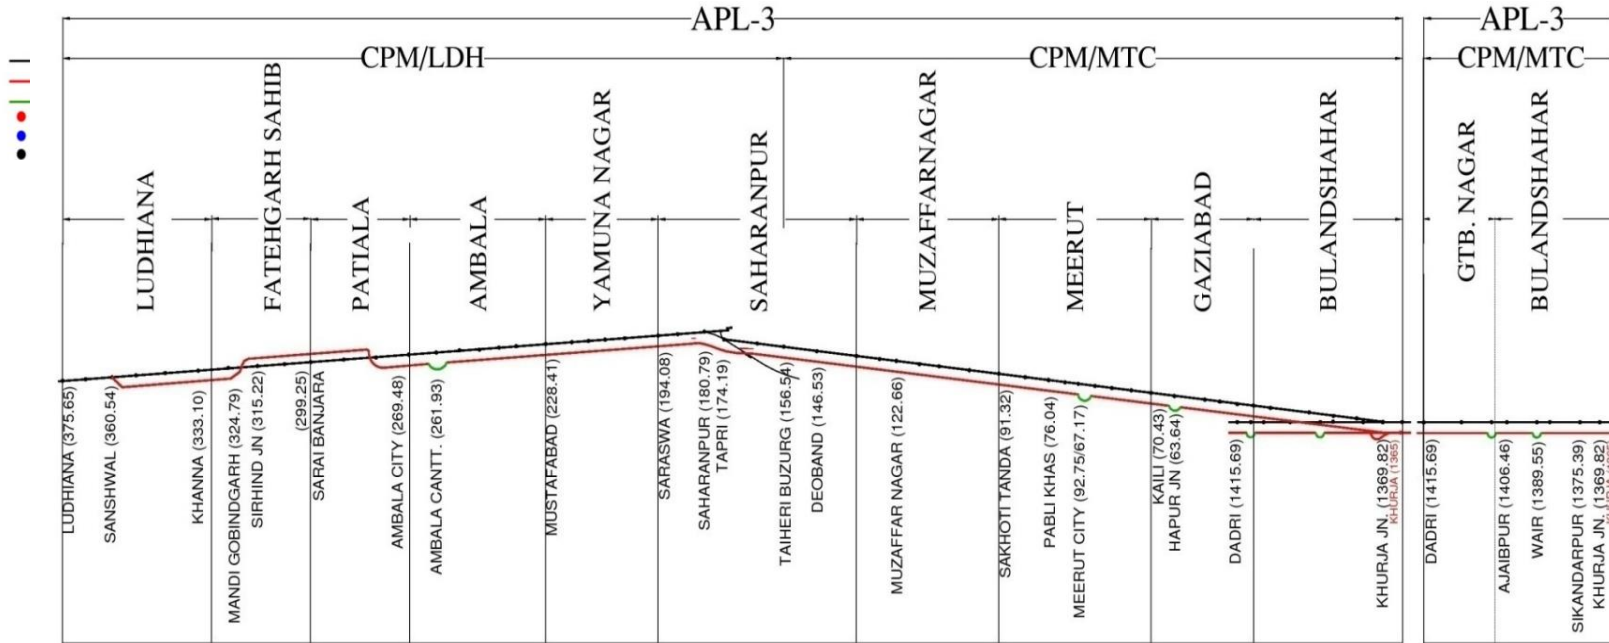

EDFC - APL-3 (Land Acquisition Progress for the Month of December 2020)

District	Ludhiana	Fatehgarh Sahib	Patiala	Ambala	Yamuna Nagar	Saharanpur	Muzaffarnagar	Meerut	Ghaziabad	Bulandshahar	GTB Nagar	Bulandshar
Scope (Kms)	33	27	27	43	29	67	44	42	40	48	19	28
Area (Ha.)	70	115	76	62	10	195	172	223	186	36	104	133
20A (Ha.)	70	115	76	62	10	195	172	223	186	36	104	133
20E (Ha.)	70	115	76	62	10	195	172	223	186	36	104	133
20F (Ha.)	70	115	76	62	10	195	172	223	186	36	104	133
Award Declared (Cr.)	327	358	291	39	10	303	632	936	759	99	355	209
Disbursed (Cr.)	307	355	274	37	8	280	603	875	720	92	309	208
Land Taken over (Ha.)	70	115	76	62	10	187	172	223	186	36	96	131
