


**LEGEND**

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

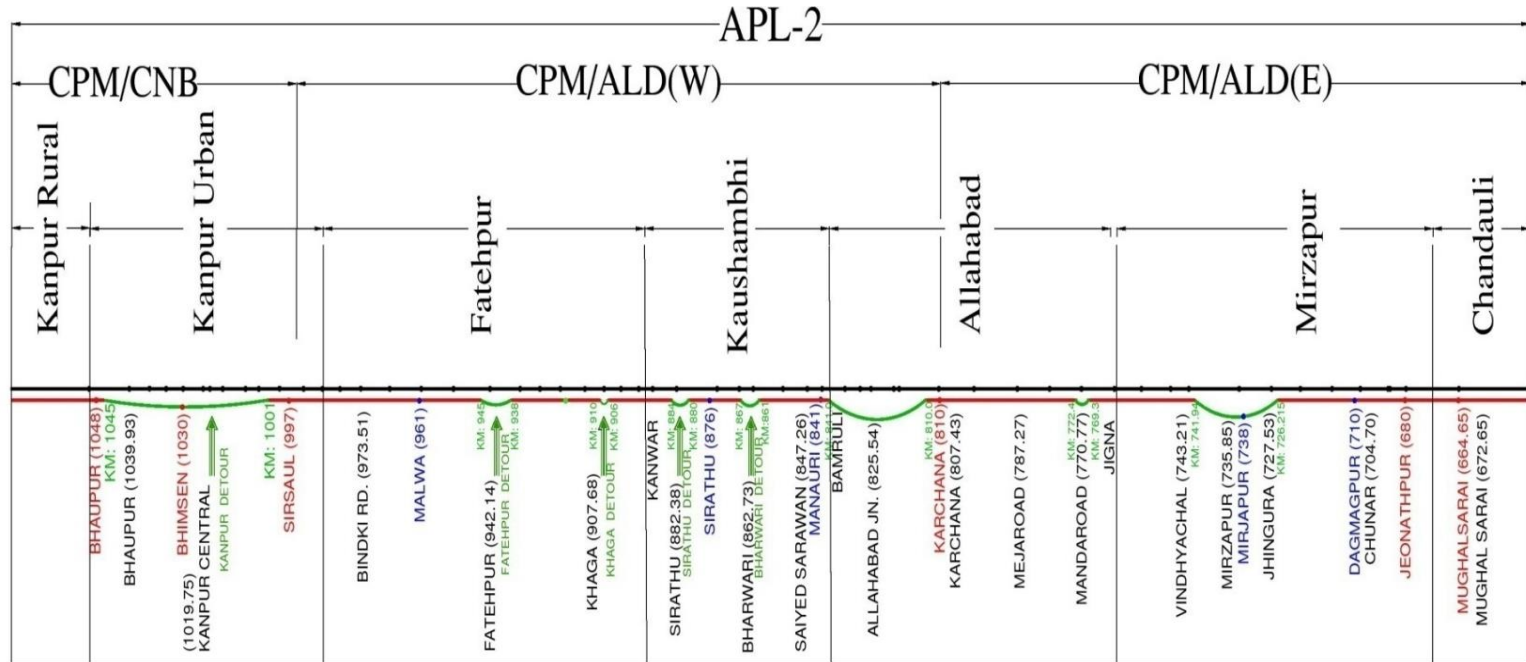

EDFC - APL – 2 (Land Acquisition Progress for the Month of September 2020)								
District	Kanpur Rural	Kanpur Urban	Fatehpur	Kaushambhi	Allahabad	Mirzapur	Chandauli	
Scope	( Kms)	6	63	104	47	84	92	24
	Area (Ha.)	16	250	168	125	416	502	23
20A (Ha.)		16	250	168	125	416	502	23
20E (Ha.)		16	250	167	125	416	502	23
20F (Ha.)		16	250	166	125	416	502	23
Award Declared (Cr.)		4	140	42	49	156	203	25
Disbursed (Cr.)		4	138	38	49	131	159	11
Land Taken over (Ha.)		14	210	138	111	405	501	22
