


**LEGEND**  
 IR TRACK  
 DFC ALIGNMENT (PARALLEL)  
 DFC ALIGNMENT (DETOUR)  
 JUNCTION STATIONS  
 X-ING STATIONS  
 IR STATIONS

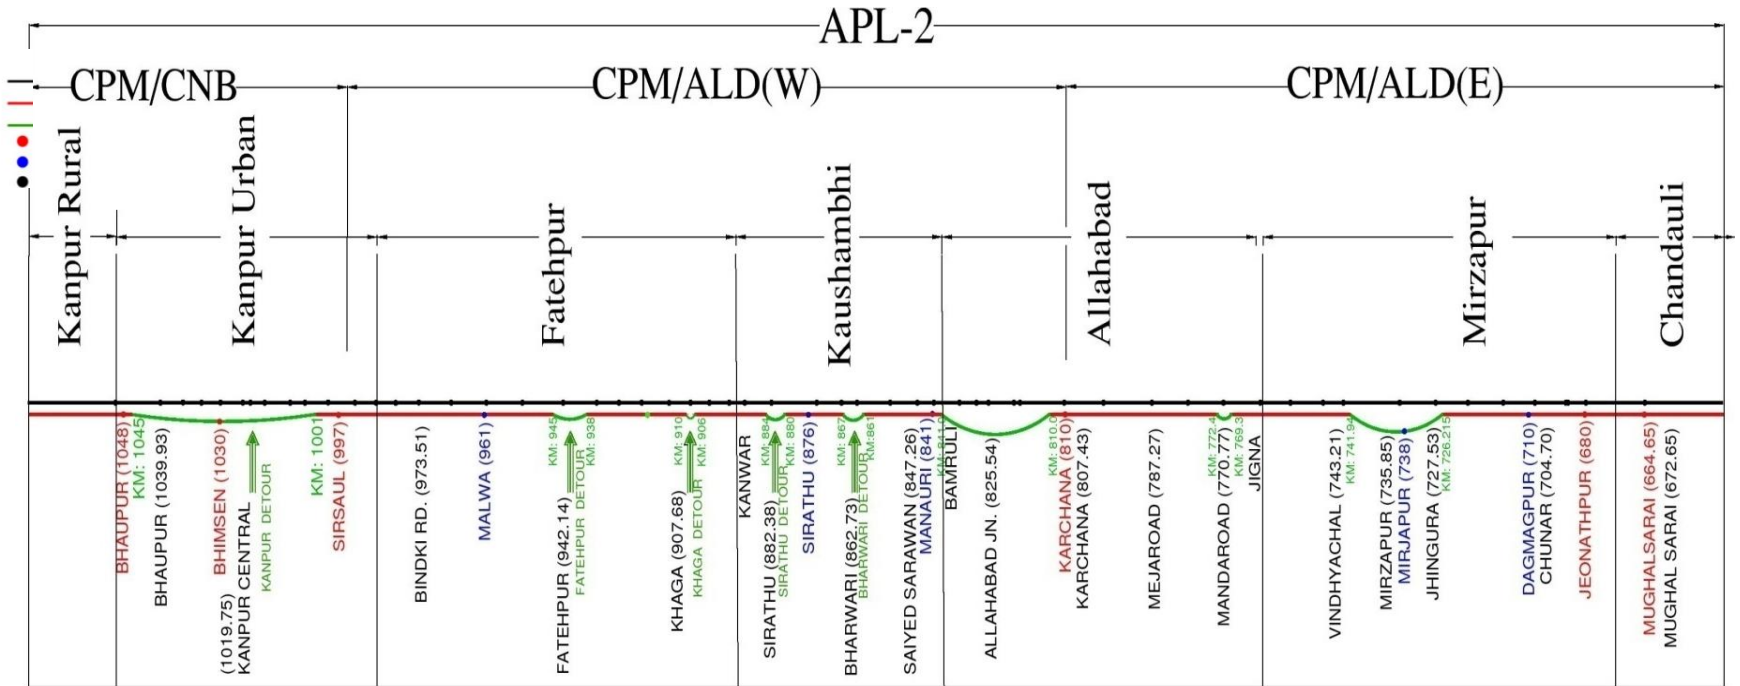

**EDFC - APL – 2 (Land Acquisition Progress for the Month of May 2021)**

District		Kanpur (Rural)	Kanpur (Urban)	Fatehpur	Kaushambhi	Allahabad	Mirzapur	Chandauli
( Kms)		6	63	104	47	84	92	24
Area (Ha.)		16	250	168	125	416	502	23
20A (Ha.)		16	250	168	125	416	502	23
20E (Ha.)		16	250	168	125	416	502	23
20F (Ha.)		16	250	168	125	416	502	23
Award Declared (Cr.)		166		60	63	187	234	26
Disbursed (Cr.)		4	156	53	61	154	185	13
Land Taken over (Ha.)		14	210	138	111	405	501	22
