


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

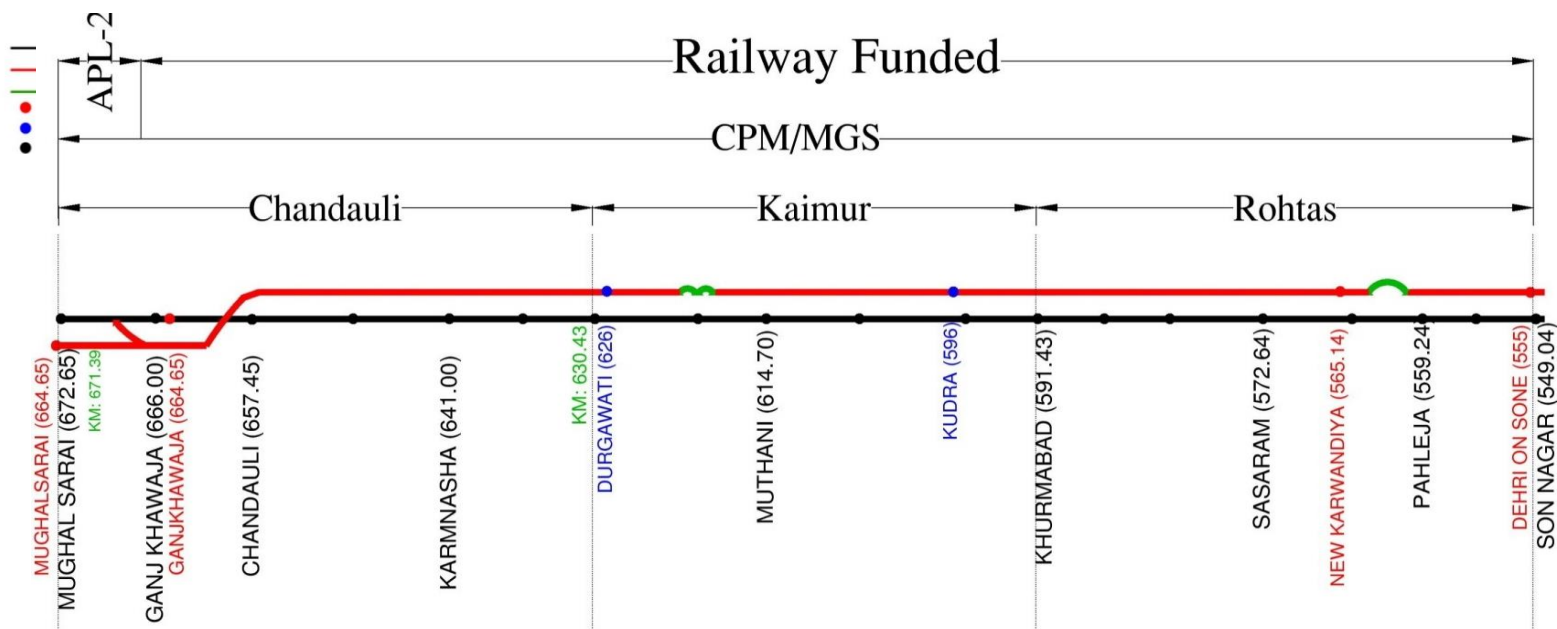

RAILWAY FUNDED (Land Acquisition Progress for the Month of May 2021)					
Districts		Chandauli - II	Kaimur	Rohtash	Auranga bad
Scope	(Kms)	26	50	40	9
	Area (Ha.)	60	114	123	37
20A (Ha.)		60	114	123	37
20E (Ha.)		60	114	123	37
20F (Ha.)		60	114	123	37
Award Declared (Cr.)		145	236	219	67
Disbursed (Cr.)		116	170	149	60
Land Taken over (Ha.)		61	110	119	28
