


LEGEND
 IR TRACK
 DFC ALIGNMENT (PARALLEL)
 DFC ALIGNMENT (DETOUR)
 JUNCTION STATIONS
 X-ING STATIONS
 IR STATIONS

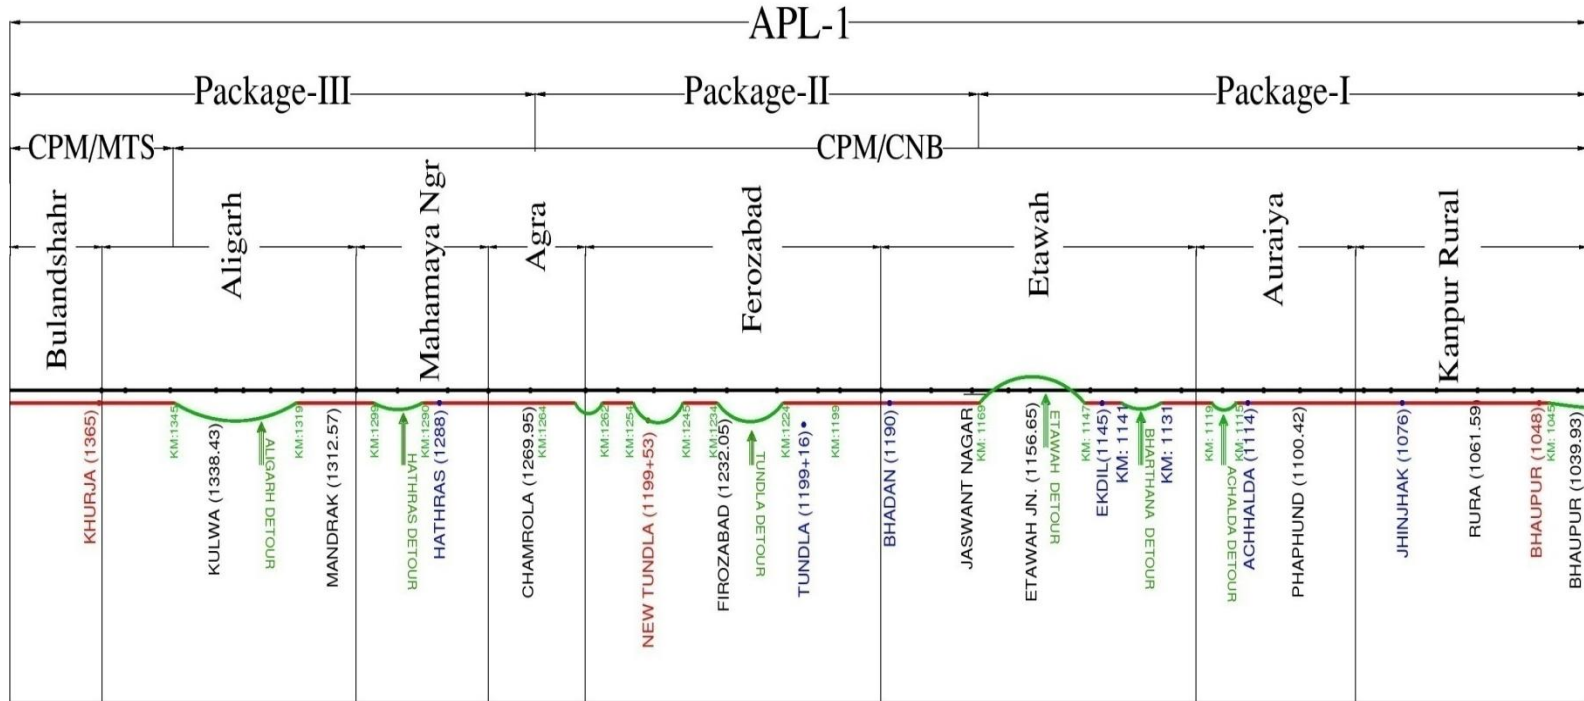

EDFC - APL-1 (Land Acquisition Progress for the Month of September 2020)

Districts		Bulandshahr	Aligarh	Mahamaya Nagar	Agra	Ferozabad	Etawah	Auraiya	Kanpur Rural
Scope	(Kms)	15	45	42	24	66	64	33	55
	Area (Ha.)	47	254	180	104	247	297	113	164
20A (Ha.)		47	254	180	104	247	297	113	164
20E (Ha.)		47	252	179	104	247	297	110	163
20F (Ha.)		47	251	175	105	247	297	110	160
Award Declared (Cr.)		46	217	110	84	139	168	46	63
Disbursed (Cr.)		36	211	109	79	138	164	43	61
Land Taken over (Ha.)		43	237	142	91	224	272	84	143

343

1405

1405

1399

1392

873

841

1236
