


**LEGEND**

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

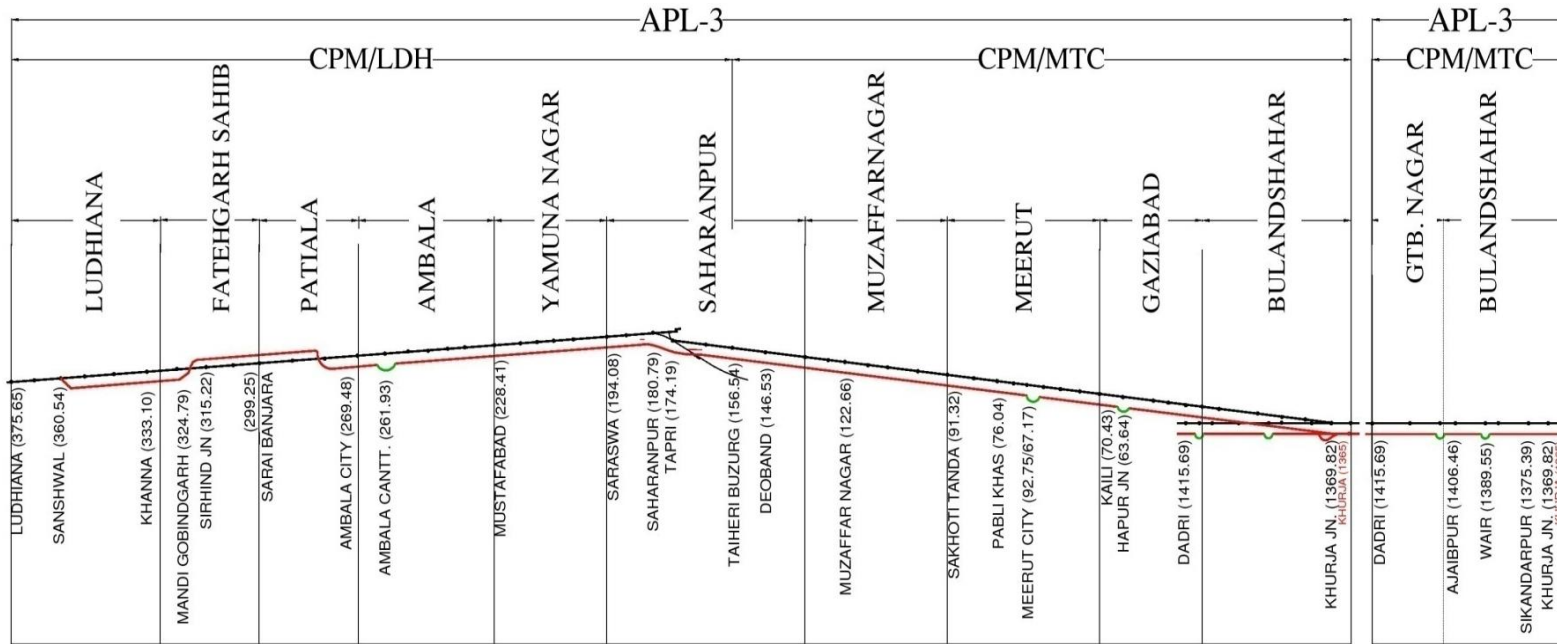

**EDFC - APL-3 (Land Acquisition Progress for the Month of September 2020)**

District		Ludhiana	Fatehgarh Sahib	Patiala	Ambala	Yamuna Nagar	Saharanpur	Muzaffarnagar	Meerut	Ghaziabad	Bulandshahar	GTB Nagar	Bulandshahar
Scope	(Kms)	33	27	27	43	29	67	44	42	40	48	19	28
	Area (Ha.)	70	115	76	62	10	195	172	223	186	36	104	133
20A (Ha.)		70	115	76	62	10	195	172	223	186	36	104	133
20E (Ha.)		70	115	76	62	10	191	171	221	177	35	104	133
20F (Ha.)		70	115	76	62	10	191	171	221	177	35	100	133
Award Declared (Cr.)		324	356	291	39	10	302	602	936	759	99	333	205
Disbursed (Cr.)		307	354	274	37	8	277	569	848	718	92	299	205
Land Taken over (Ha.)		68	115	72	45	9	187	172	162	168	112	96	131
