


**LEGEND**

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

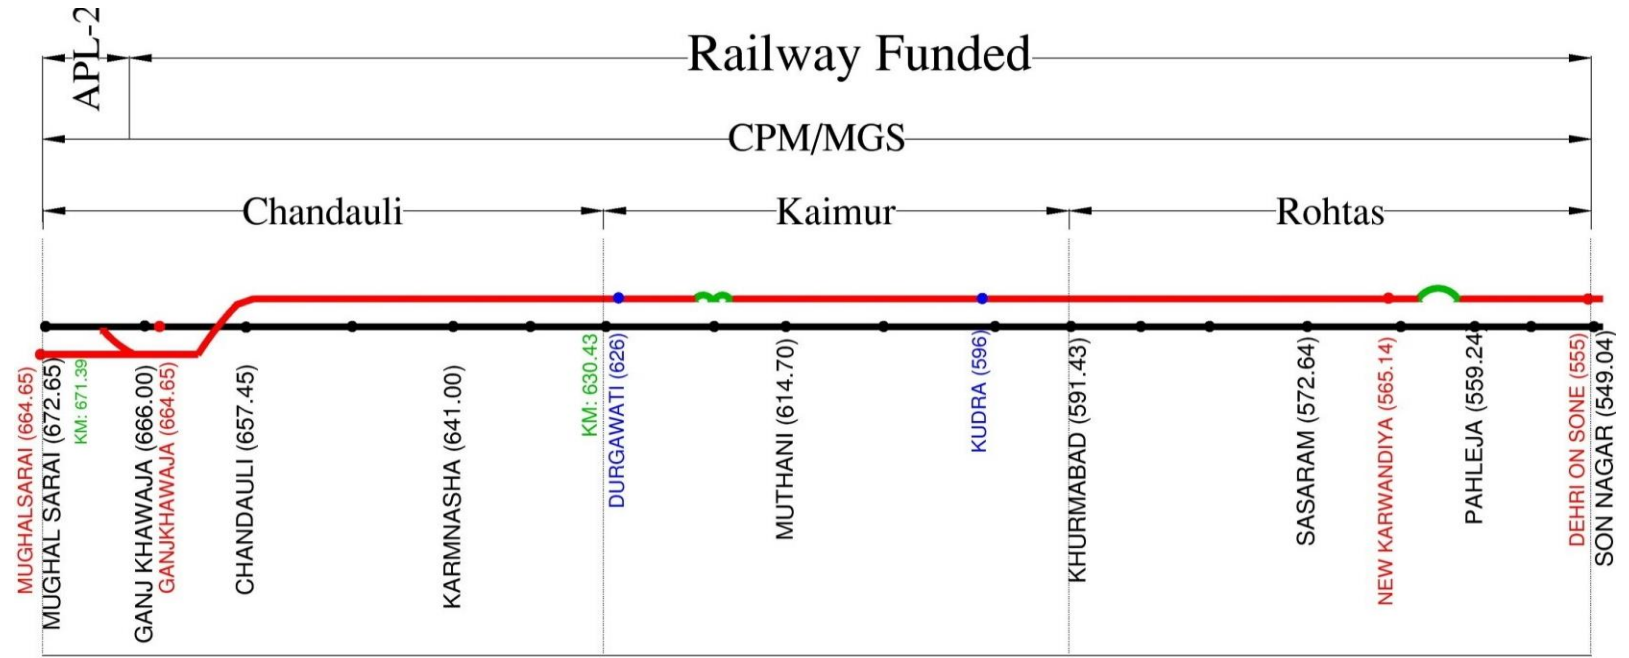

RAILWAY FUNDED (Land Acquisition Progress for the Month of September 2020)					
District		Chandauli	Kaimur	Rohtash	Aurangabad
Scope	( Kms)	25.53	50.37	40.07	9.2
	Area (Ha.)	59.78	113.87	122.85	36.85
20A (Ha.)		59.78	113.87	122.85	36.85
20E (Ha.)		59.78	113.87	122.85	36.85
20F (Ha.)		59.78	113.87	122.85	36.85
Award Declared (Cr.)		144.76	236.23	218.89	67.36
Disbursed (Cr.)		102.98	145.6	144	53
Land Taken over (Ha.)		48.31	88.09	117.84	25.09
