


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

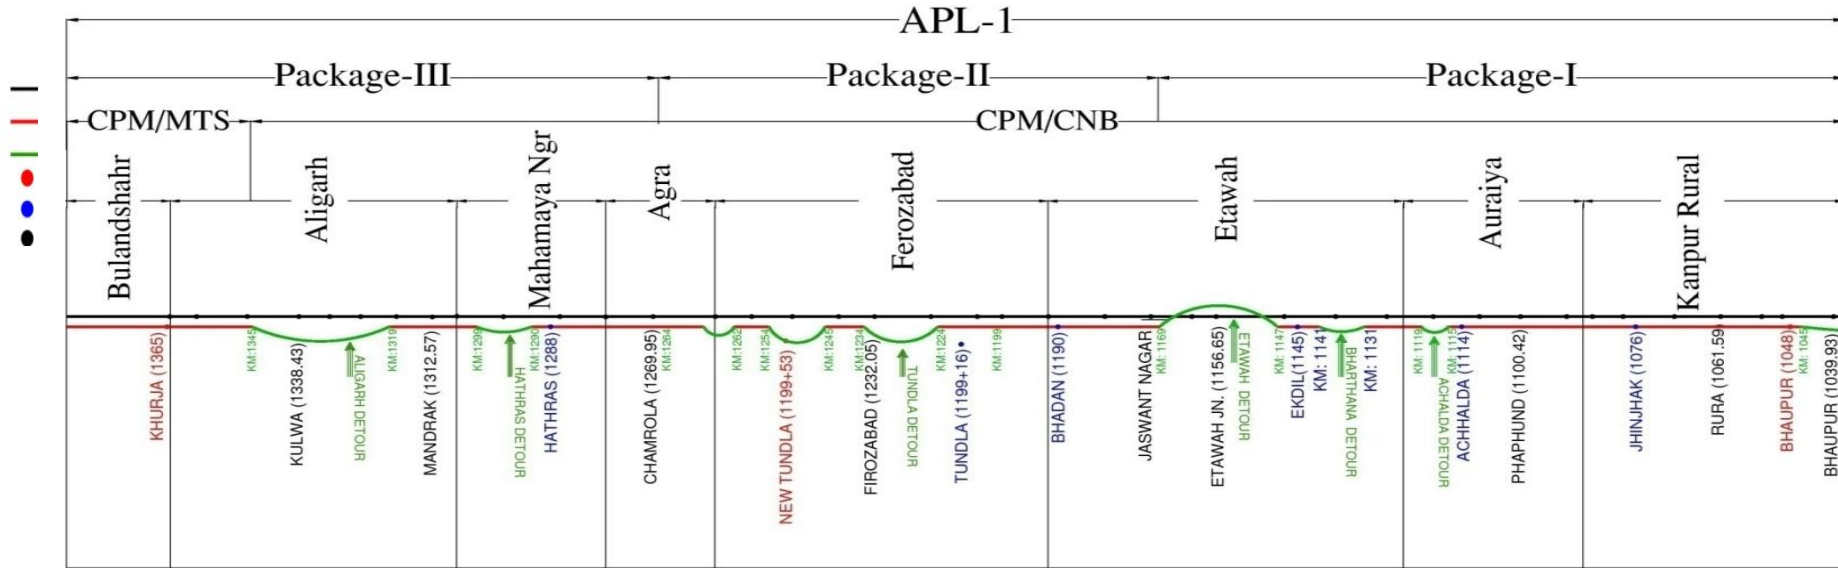

पूर्वी डेडीकेटेड फ्रेट कोरीडोर - एपीएल-1 (भूमि अधिग्रहण प्रगति)

EDFC - APL-1 (Land Acquisition Progress)

Scope	(Kms)	15	45	42	24	66	64	33	55
	Area (Ha.)	47	254	180	104	247	297	113	164
20A (Ha.)	47	254	180	104	247	297	113	164	
20E (Ha.)	48	249	177	104	246	293	110	160	
20F (Ha.)	47	244	168	103	245	292	110	157	
Award Declared (Cr.)	26	185	88	73	119	114	15	26	
Disbursed (Cr.)	21	160	85	63	113	89	14	24	
Land Taken over (Ha.)	39	211	163	89	232	228	105	141	
