


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

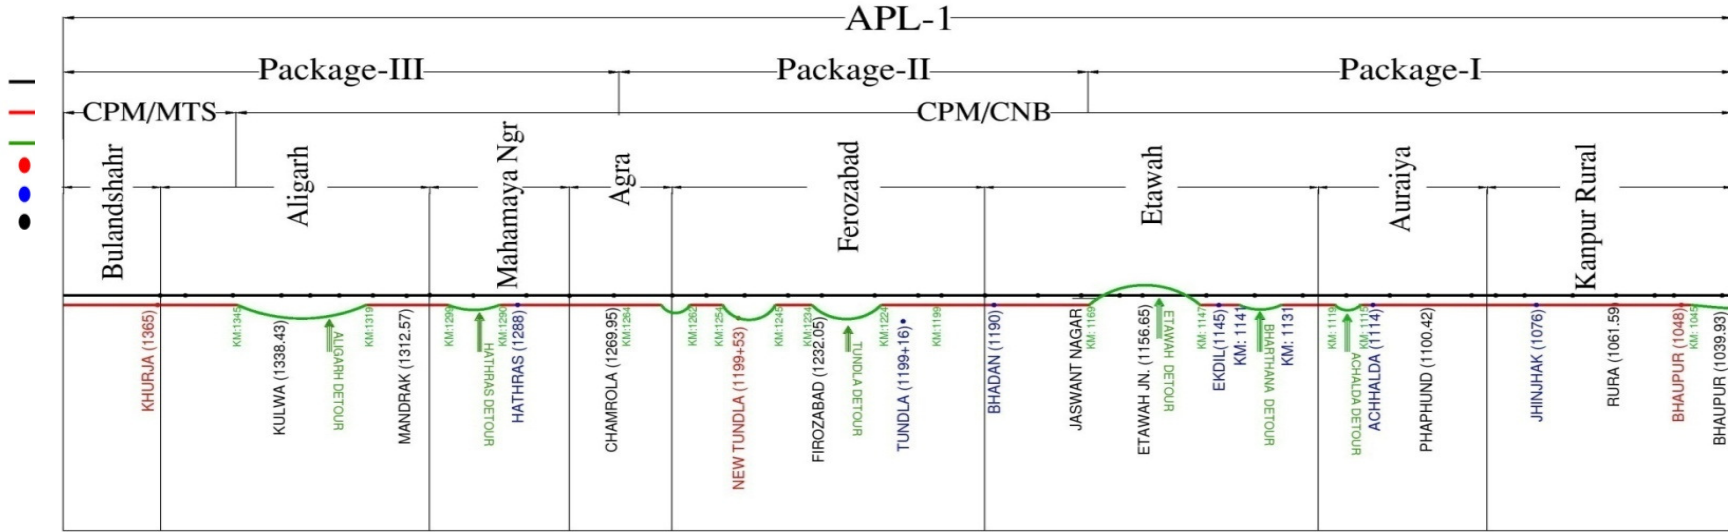

पूर्वी डेडीकेटेड फ्रेट कोरिडोर - एपीएल-1 (भूमि अधिग्रहण प्रगति)

EDFC - APL-1 (Land Acquisition Progress for)

Scope	(Kms)	15	45	42	24	66	64	33	55
	Area (Ha.)	61	256	176	103	245	297	109	161
20A (Ha.)	59	253	174	97	240	292	107	154	
20E (Ha.)	59	241	168	97	240	292	107	154	
20F (Ha.)	59	237	167	97	238	292	107	154	
Award Declared (Cr.)	26	158	87	64	114	60	14	18	
Disbursed (Cr.)	20	144	77	50	107	44	13	15	
Land Taken over (Ha.)	46	216	147	77	222	214	99	129	
