


Land Acquisition November 2018

Section Wise Progress of Land Acquisition for the month of November 2018		Total Scope				20 A		20 E		20 F		Amount (in Crs.)	
		Length (Km.)	Pvt. Land	Govt. Land	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Award	Disbursement
Western Corridor													
Phase-I Rewari- Vadodara	Haryana	81	252	1	252	81	252	81	252	81	252	259	256
	Rajasthan	552	1349	475	1824	552	1824	552	1824	552	1823	321	297
	Gujarat	321	1469	171	1640	321	1640	321	1640	321	1639	908	832
Total		954	3070	647	3716	954	3716	954	3716	954	3714	1488	1385
Phase-II Vadodara- JNPT & Rewari- Dadri	Gujarat	244	734	79	813	244	813	244	813	246	806	971	902
	Maharashtra	177	264	181	444	177	444	177	444	147	415	1136	893
	Haryana	96	713	6	719	96	719	96	719	96	719	1556	1454
	Rajasthan	16	88	44	132	16	132	16	132	16	132	267	257
	Uttar Pradesh	19	94	82	175	19	175	19	175	19	175	568	577
Total		551	1893	391	2283	551	2283	551	2283	524	2247	4498	4083
Total of WDFC		1505	4962	1037	6000	1505	6000	1505	5999	1477	5961	5986	5468

Phase-I Rewari-Vadodara

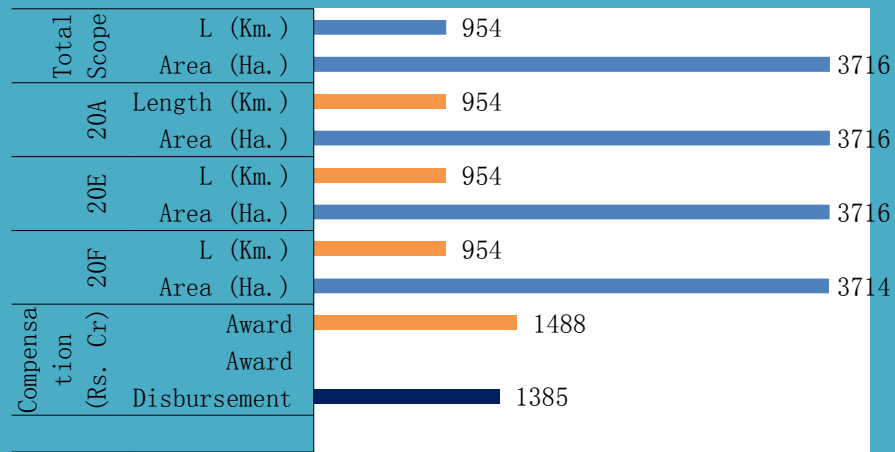

Phase-II Vadodara-JNPT & Rewari-Dadri

