


LEGEND

- IR TRACK
- DFC ALIGNMENT (PARALLEL)
- DFC ALIGNMENT (DETOUR)
- JUNCTION STATIONS
- X-ING STATIONS
- IR STATIONS

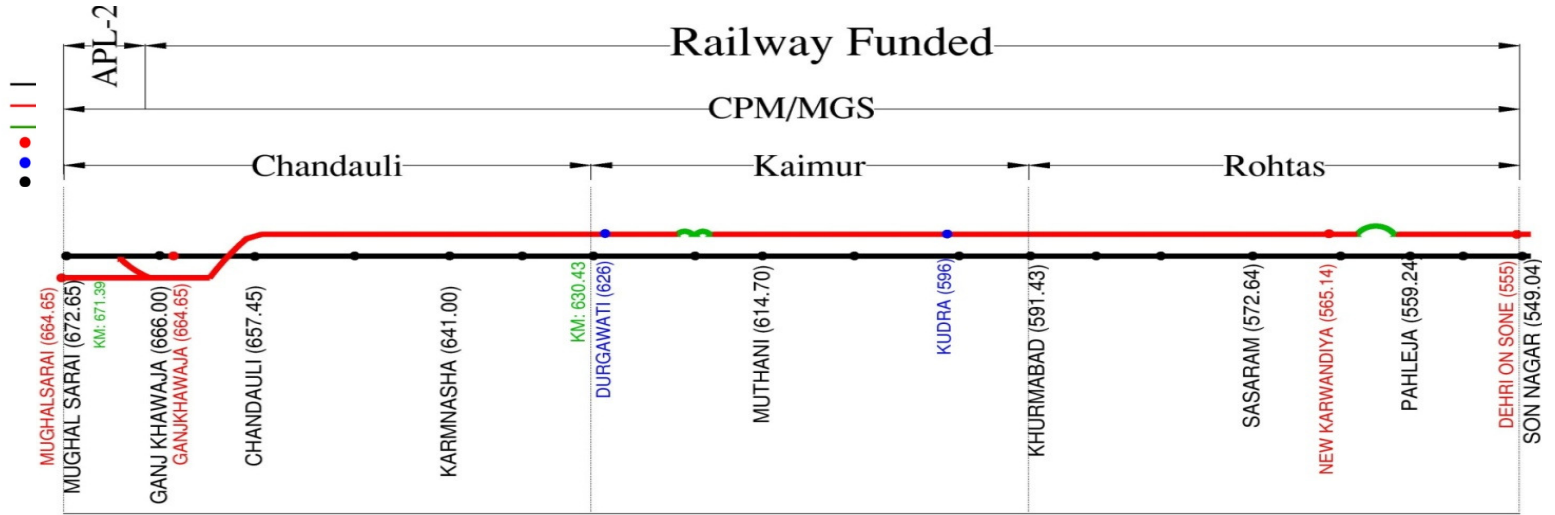

रेलवे फंडेड (भूमि अधिग्रहण प्रगति)

RAILWAY FUNDED (Land Acquisition Progress)

Scope	(Kms)	28	51	40
	Area (Ha.)	65	84	105
20A (Ha.)		65	84	105
20E (Ha.)		59	81	104
20F (Ha.)		57	81	98
Award Declared (Cr.)		36	108	106
Disbursed (Cr.)		21	77	89
Land Taken over (Ha.)		33	57	82
