
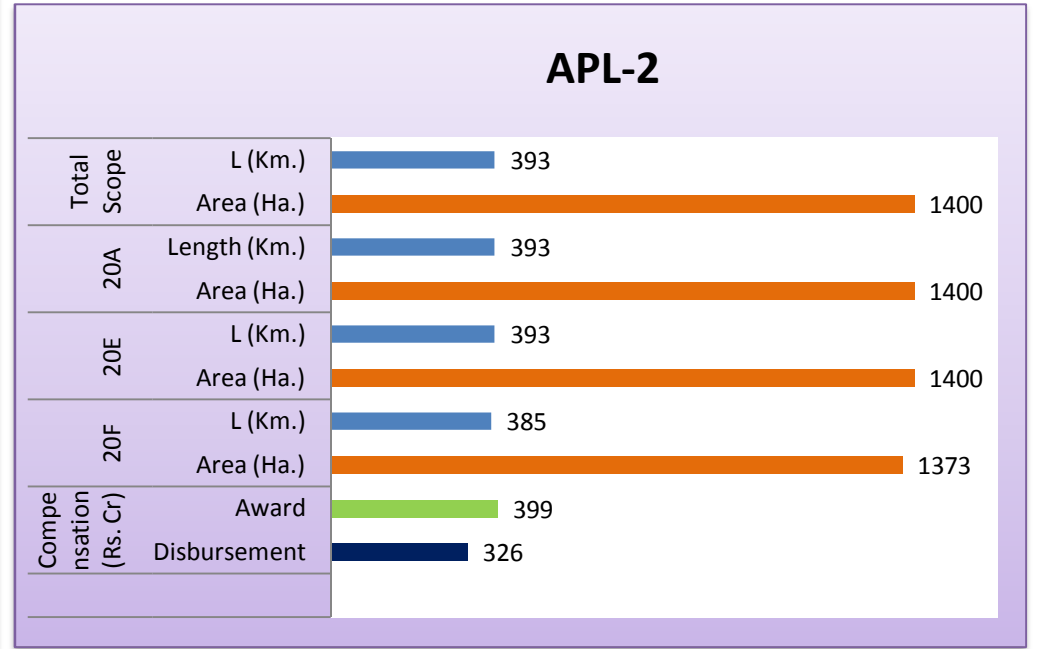



भूमि अधिग्रहण माह अप्रैल, 2014 Land Acquisition for the month of April, 2014

परियोजना विवरण Project Description		कुल क्षेत्र Total Scope			20 A		20 E		20 F		Amount (in Crs.)	
		Length (Km.)	Govt. Land	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Length (Km.)	Area (Ha.)	Award	Disbursement
पूर्वी कोरीडोर Eastern Corridor												
APL- 1 (खुर्जा-भाऊपुर खंड) Khurja - Bhaupur Section)	उत्तर प्रदेश Uttar Pradesh	343	178	1320	343	1320	343	1320	341	1315	543	516
कुल Total		343	178	1320	343	1320	343	1320	341	1315	543	516
APL- 2 (भाऊपुर-मुगलसराय खंड) Bhaupur - Mughalsarai Section)	उत्तर प्रदेश Uttar Pradesh	393	205	1400	393	1400	393	1400	385	1373	399	326
कुल Total		393	205	1400	393	1400	393	1400	385	1373	399	326
APL- 3 (लुधियाना-खुर्जा खंड) Ludhiana - Khurja Section)	पंजाब Punjab	88	33	251	88	251	88	251	88	251	816	764
	हरियाणा Haryana	72	34	78	72	78	72	78	72	78	36	31
	उत्तर प्रदेश Uttar Pradesh	288	81	436	269	353	263	338	263	338	231	114
कुल Total		447	148	766	428	682	422	667	422	667	1083	908
रेलवे पोषित (मुगलसराय-सोननगर खंड) Railway Funded (Mughalsarai - Sonnagar Section)	उत्तर प्रदेश Uttar Pradesh	26	1	51	26	51	25	46	24	42	26	18
	बिहार Bihar	93	14	268	93	268	91	263	90	259	208	153
कुल Total		118	15	319	118	319	115	309	113	301	234	171
सोननगर-दानकुण्ड	बिहार Bihar	139	65	202	118	189	91	121	91	121	58	0

(Sonnagar-Dhankuni)	Jharkhand	196	175	373	164	184	104	135	106	135	112	0
	West Bengal	203	37	427	203	427	149	235	123	127	69	0
Total		538	277	1002	485	799	344	490	320	383	238	0
Total of EDFC		1839	822	4807	1767	4520	1618	4186	1581	4038	2497	1921

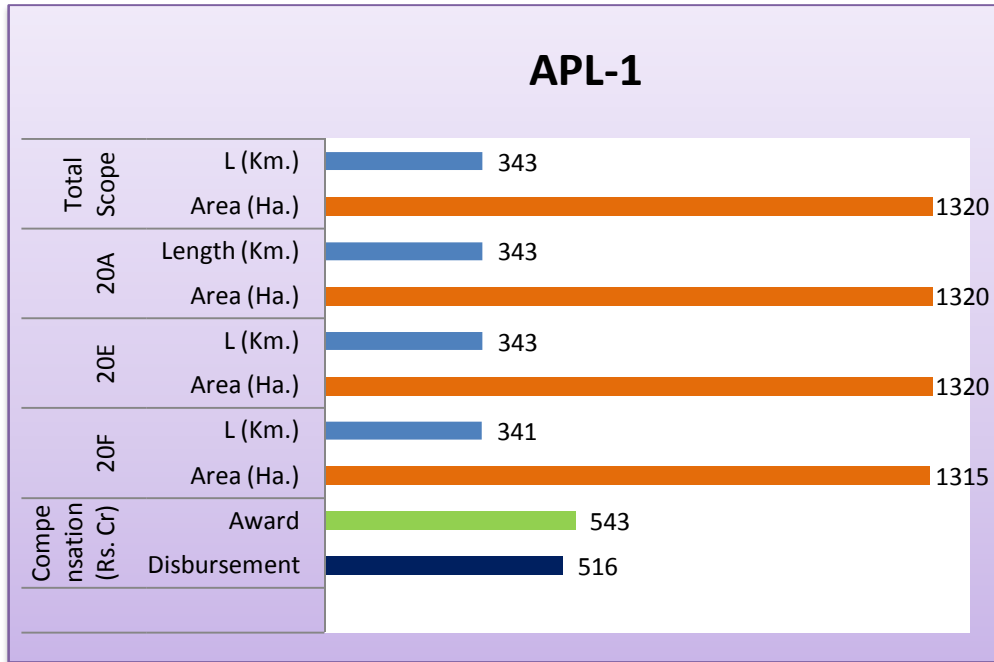

APL-3

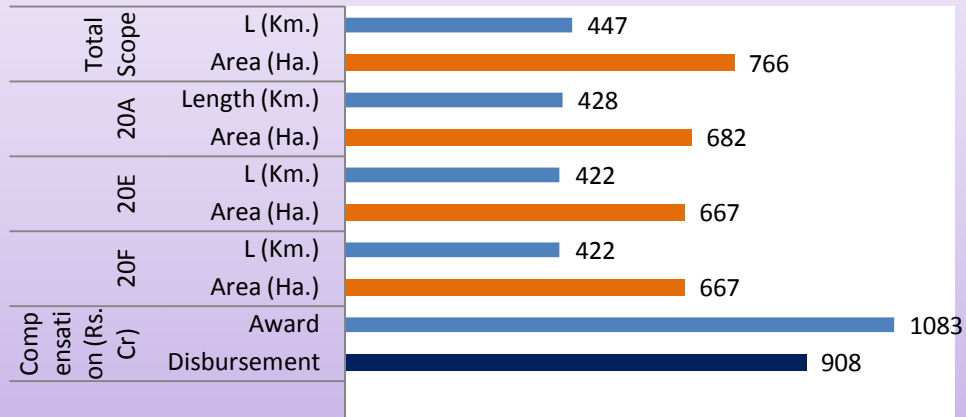

- Railway Funded (Mughal Sarai-Sonnagar)

